Superior Court Data Exchange

Project Status

Mike Walsh, Project Manager

September 7, 2012

Superior Court Data Exchange Project

As of July 1, 2012 Mike Walsh has taken over project management responsibilities for the SCDX project.

Increment 1 Status:

✓ QA Testing Completed.

- All 10 web services were successfully tested.
- Low defect rate with no significant changes.
- Web Services will be available in Production by Aug. 29, 2012.

Superior Court Data Exchange Project

Increment 2 Status :

- ✓ All nineteen web services were delivered by June 11, 2012.
- ✓ Increment 2 QA testing preparation started July 23, 2012.
- ✓ One additional tester was added July 30, 2012.
- ❑ Second tester starts Aug. 27, 2012.
- ❑ Test tool delivery, which is expected to reduce test effort and duration, is scheduled for Aug. 24, 2012.
- ❑ QA Testing is planned to finish Oct. 19, 2012.

Superior Court Data Exchange Project

Increment 3 Status:

- ✓ All twelve web services were delivered by Aug. 3, 2012.
- ❑ QA Testing is scheduled to start Oct. 9, 2012.
- ❑ QA Testing is scheduled to finish Dec. 21, 2012.

Superior Court Data Exchange Project

Increment 4:

- Twenty five web services scheduled to be delivered by Nov. 30, 2012.
  - Twelve web services in contract with Sierra.
    - ✓ Work started on Aug. 1, 2012.
  - Thirteen web services assigned to AOC Staff.
    - ✓ Two web services have been developed.
    - ✓ Work started on July 1, 2012.
    - ✓ Two web services have been developed.
  - Sierra delivery scheduled to complete Oct. 31, 2012.
  - AOC Development scheduled to complete Nov. 30 2012.
  - QA Testing scheduled to start Dec.24 2012.
  - QA Testing scheduled to finish May 6, 2013.

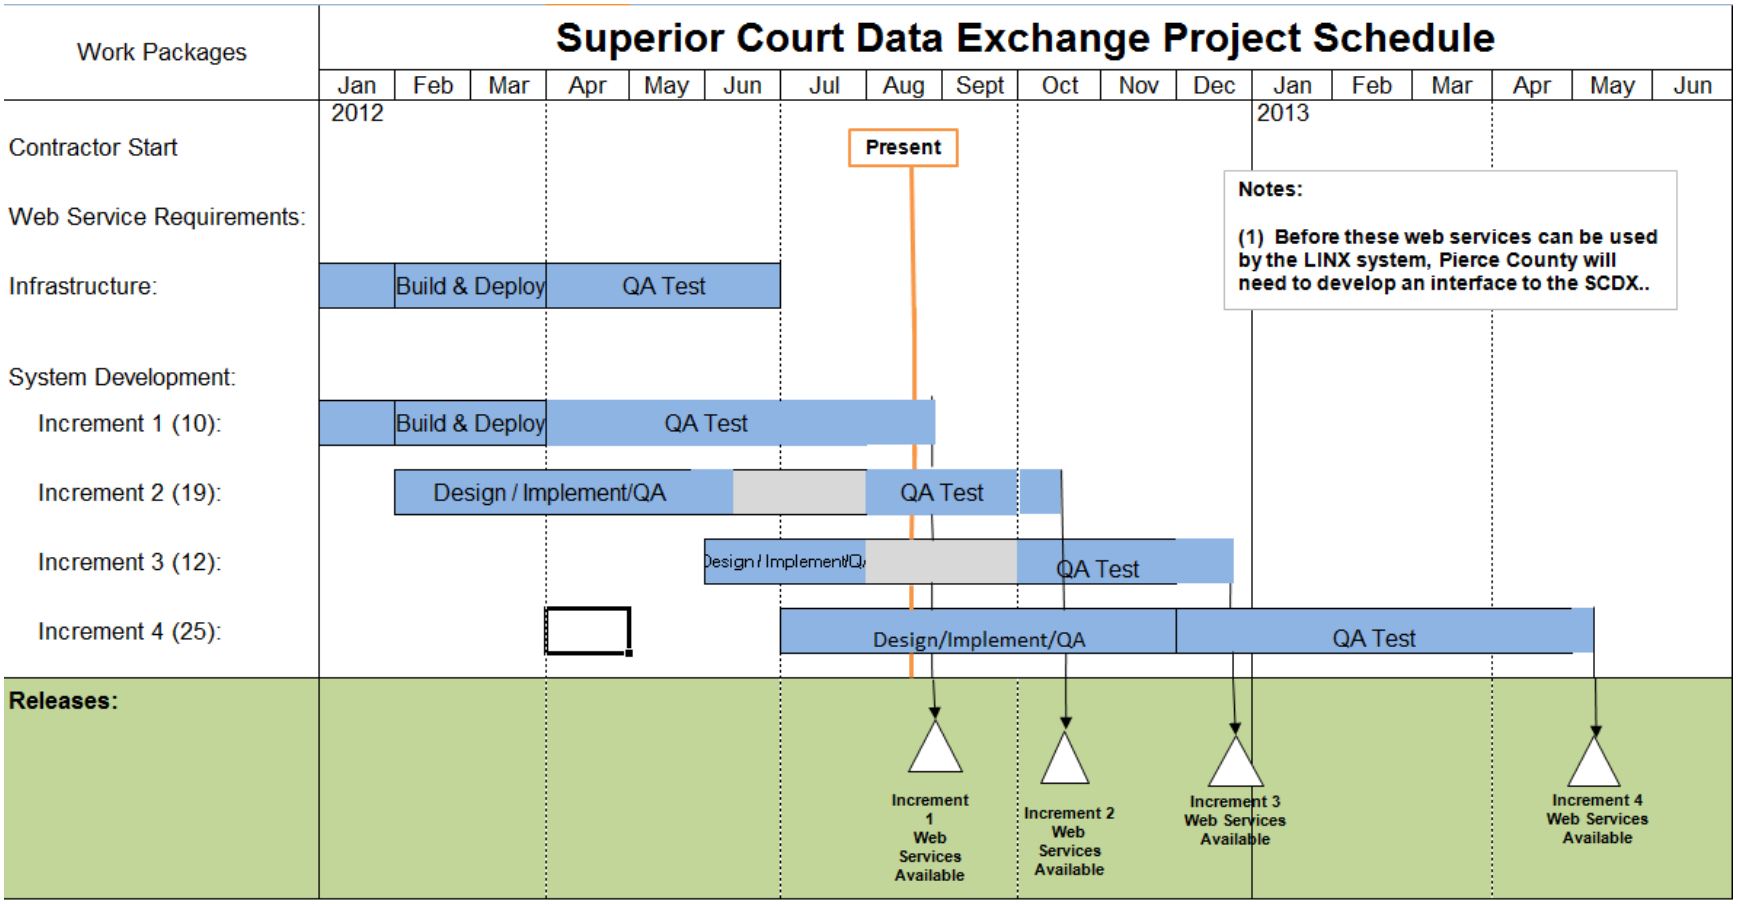
Superior Court Data Exchange Project Schedule
Work Packages
Jan Feb Mar Apr May Jun Jul Aug Sept Oct Nov Dec Jan Feb Mar Apr May Jun
2012
2013
Contractor Start
Present
Web Service Requirements:
Notes:
(1) Before these web services can be used by the LINX system, Pierce County will need to develop an interface to the SCDX..
Infrastructure:
Build & Deploy
QA Test
System Development:
Increment 1 (10):
Build & Deploy
QA Test
Increment 2 (19):
Design / Implement/QA
QA Test
Increment 3 (12):
Design / Implement/QA
QA Test
Increment 4 (25):
Design/Implement/QA
QA Test
Releases:
Increment 1 Web Services Available
Increment 2 Web Services Available
Increment 3 Web Services Available
Increment 4 Web Services Available

Superior Court Data Exchange
Active Project Issues

Issue	Category	Action
Test turn around impacting schedule	High/High	• Added two testers • Acquired test tool from Sierra Systems • Revised testing methods • Grouped test assignments • Improved test planning • Reviewing test coverage options

Superior Court Data Exchange Project
High-Level Architecture

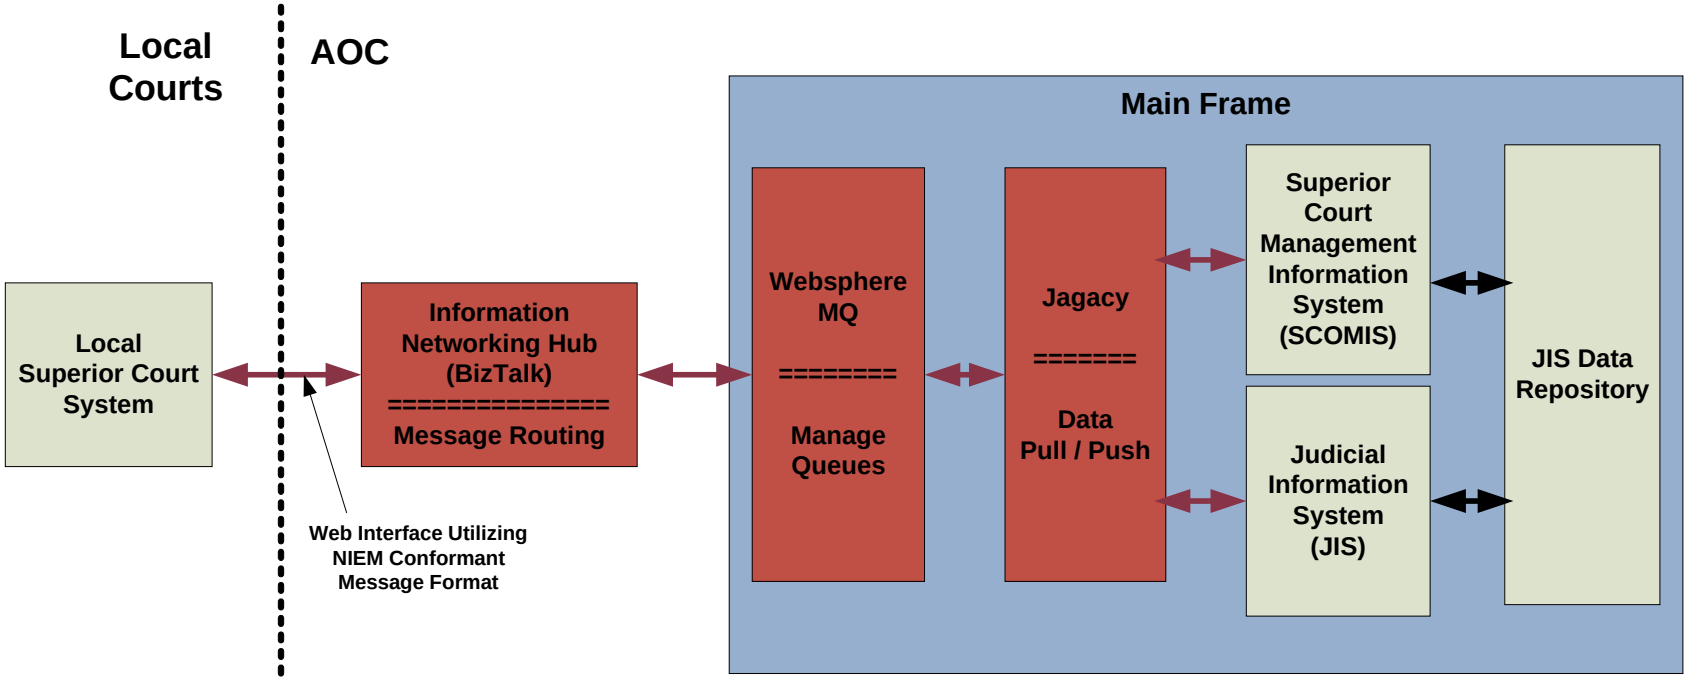



- Color denotes areas of SCDX project development
