Superior Court Data Exchange

Project Status

Mike Walsh, Project Manager

December 7, 2012

Superior Court Data Exchange Project

Increment 1 Status (10 web services):

- Pierce is planning to start using their docket web services on December 3rd.

Superior Court Data Exchange Project

Increment 2 Status (19 web services):

- ✓ Significant improvements have been made by the test team.
  - Test tools acquisitions are proving their value.
  - Team of three testers are exceeding our schedule expectations.
- ✓ Initial round of testing complete.
  - Defect fixes, re-tests, and regression testing in progress.
- ❑ Increment 2 scheduled for a November deployment.

Superior Court Data Exchange Project

Increment 3 Status (12 web services):

- ✓ Sierra developed and delivered all 12 web services by Aug. 3, 2012.
- ➢ QA Testing started November 8, 2012.

Superior Court Data Exchange Project

Increment 4 (25 web services):

- ✓ All 25 web services have been developed and delivered.
  - ✓ Sierra delivered all12 web services by October 3, 2012.
    - ➢ Finished 3 weeks ahead of schedule.
  - ✓ AOC Staff completed development of their 13 web services by November 9, 2012.
    - ➢ Finished 3 weeks ahead of time.

Superior Court Data Exchange Project

Revised Roll Out Strategy

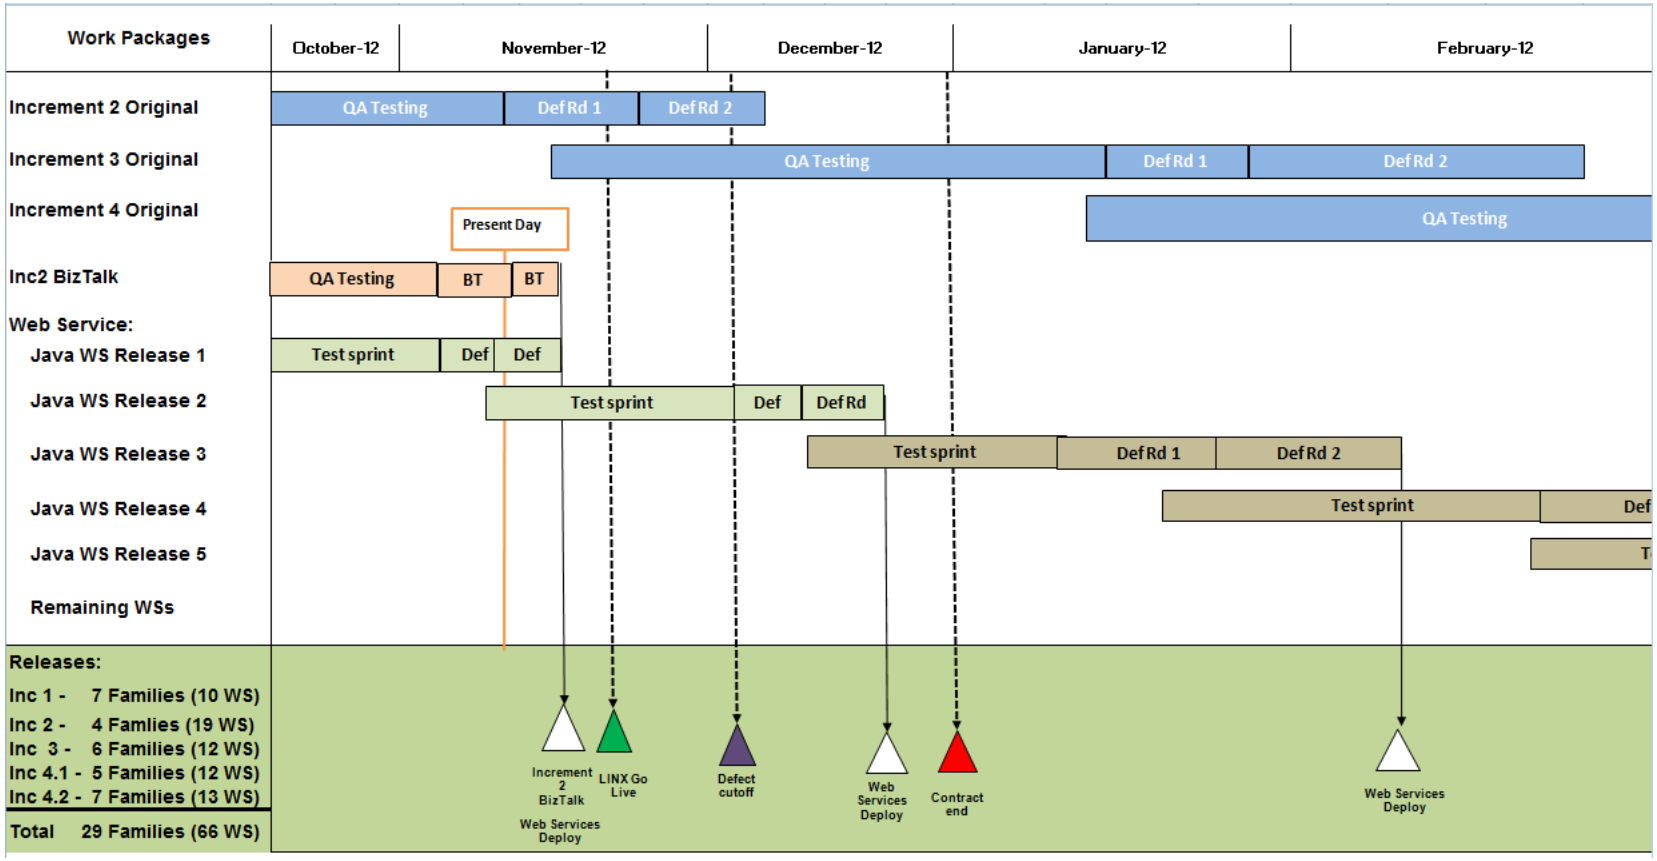

Superior Court Data Exchange Project

Testing Impact Addressed with Revised Roll Out Strategy:

- Testing turnaround has been improved.
- The new strategy creates a more efficient web service release schedule.
  - Provides a “release when ready” roll out of new services.
  - Leverages the improvements made by the testers.
  - Sierra contract ending this month, so contract constraints on service delivery are removed.
  - Web service support will transition to AOC data exchange operations.

Active Project Risks

Total Project Risks		
Low Exposure	Medium Exposure	High Exposure
1	1	1

Significant Risks Status

Risk	Severity/Impact	Mitigation
Defect corrections for INC 3 and 4 will be handled by AOC staff.	High/High	• Create an agile-like pattern by providing a regular release schedule. • Provides a “release when ready” roll out strategy for new services

Active Project Issues

Total Project Issues			
Low Urgency	Medium Urgency	High Urgency	Closed
0	1	0	0

High Urgency Issues Status

Issue	Category	Action
Test turn around impacting schedule	High/Med	• Downgraded from high/high based on testing turnaround improvement and revised roll out strategy.
