Superior Court Data Exchange

Project Update

Mike Walsh, PMP - Project Manager

February 22, 2013

Recent Activities

Contract complete with Sierra/CodeSmart

- ✓ Defects submitted through December 3rd were resolved and retested successfully
- ✓ Contractor has met all the delivery commitments of the contract

Recent Activities

Increment 1 Status (10 web services):

- Pierce County has uncovered some significant issues while testing the docket web services
  - ✓ Technical problem with framework caused Pierce web services to suspend. (Resolved mid-December)
  - ✓ Docket entries submitted out of file date order create an incorrect case status in SCOMIS
    - ➢ Correction will require major program changes for both the AOC and Pierce County data exchanges
- Pierce County's ability to use the data exchanges is delayed until corrections are in place
- Pierce County will continue to test other web services as planned

Recent Activities

Increment 2 Status (19 web services):

- ✓ Seven web services are ready for Pierce to start using
- ✓ Twelve are scheduled for deployment in February

Increment 3 Status (12 web services):

- AOC staff continues testing
- Support for defect correction has transitioned from Contractor to AOC staff

Schedule

Revised Roll Out Strategy

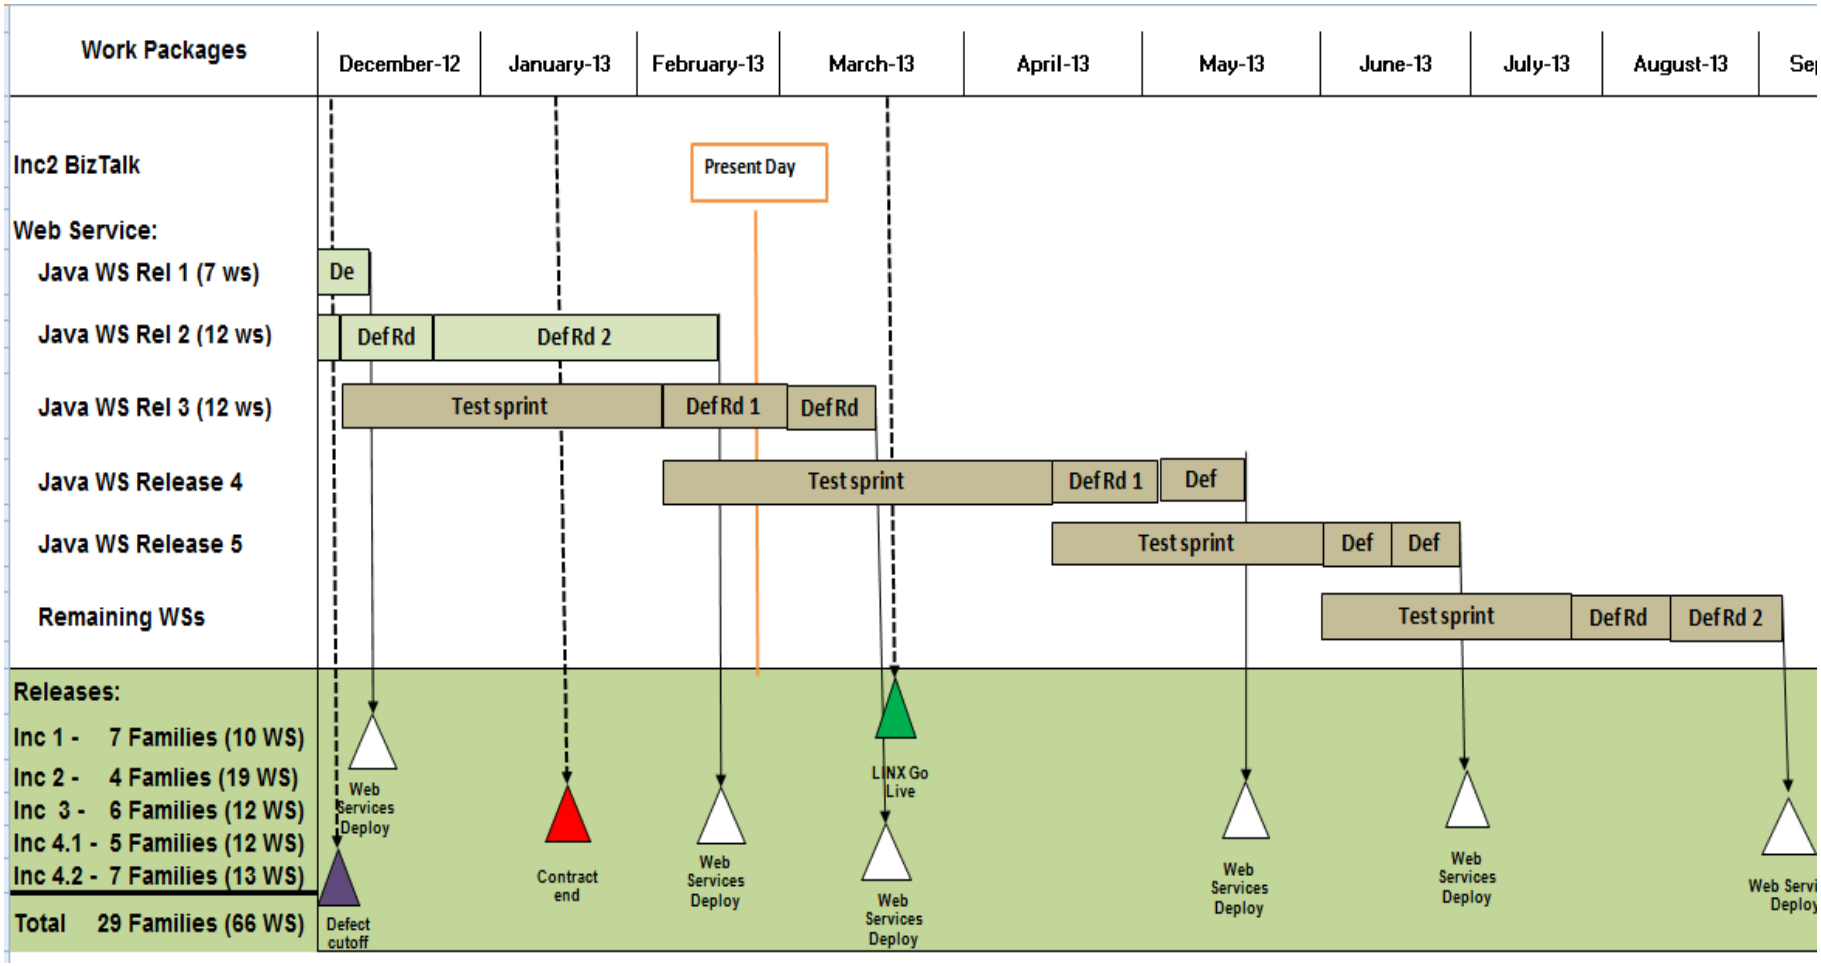

Active Project Risks

Total Project Risks		
Low Exposure	Medium Exposure	High Exposure
0	0	1

Significant Risks Status

Risk	Probability/Impact	Mitigation
Timeliness of defect corrections.	High/High	• Provides a “release when ready” roll out strategy for new services

Active Project Issues

Low Urgency	Medium Urgency	High Urgency	Closed
0	0	3	0

High Urgency Issues Status

Issue	Urgency/Impact	Action
Test turn around impacting schedule	High/Med	• Continue to monitor and adjust
Pierce Docket entry sequence causes erroneous case status in SCOMIS	High/High	• Changes to both the Pierce County sending services and the AOC receiving services
Field truncation	High/High	•Pierce County will apply truncation rules when generating the web service request

Next Steps

Milestone	Date
Resolve Docketing Order Defect	March 2013
Complete initial testing of all services	July 2013
Support Pierce County and any other customers starting to consume services	On-going
