Information Networking Hub (INH)

Project Update

Dan Belles, PMP - Project Manager

April 25, 2013

INH – Odyssey Integration Recent Activities

SC-CMS Pilot Court Readiness

- Party (Person) Data Replication – Between JIS and Odyssey
  - Requirements Analysis
  - Solution Design
  - Development/Prototyping
  - Test Strategy Development
- DOL Person Lookup Service – Requirements Analysis
- JCS Financials Support – Requirements Analysis

Schedule

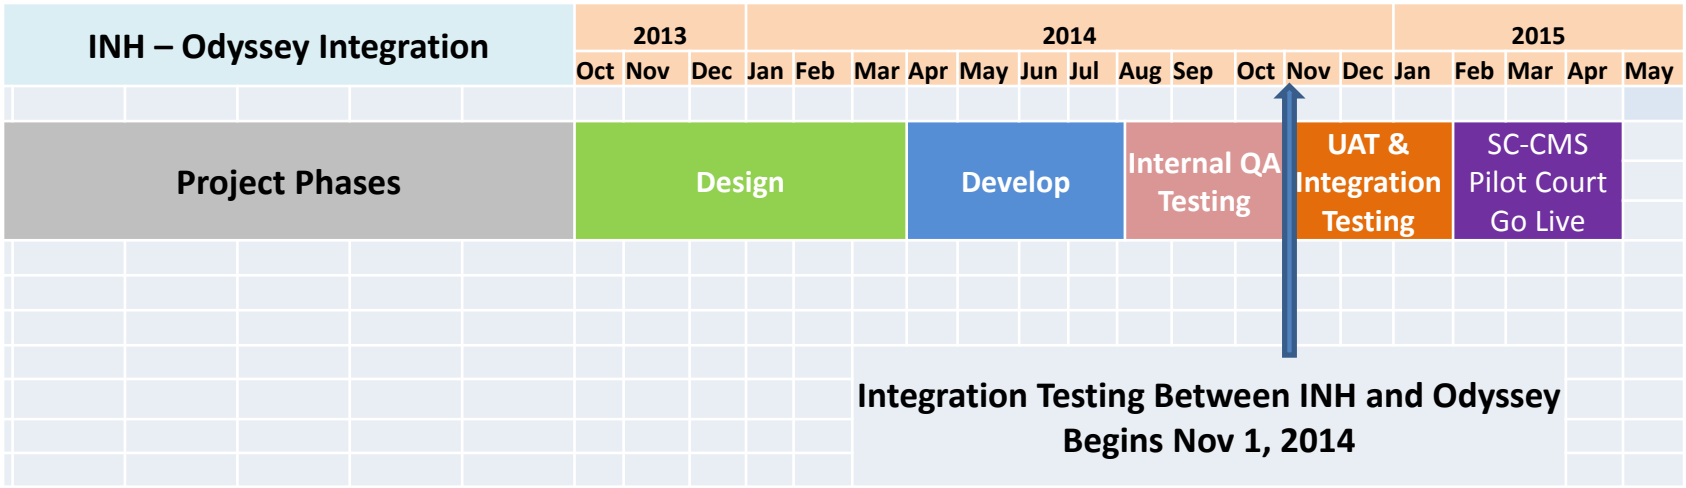
INH – Odyssey Integration
2013
2014
2015
Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May
Project Phases
Design
Develop
Internal QA Testing
UAT & Integration Testing
SC-CMS Pilot Court Go Live
Integration Testing Between INH and Odyssey Begins Nov 1, 2014

Active Project Risks

Total Project Risks		
Low Exposure	Medium Exposure	High Exposure
0	0	2

Significant Risks Status

Risk	Probability/Impact	Mitigation
Critical Project Inter-dependencies	High/High	• Inter-dependent Project Coordination Team (IPCT)
INH Integration with Odyssey	High/High	• Collaborate with SC-CMS technical team and Tyler to define requirements
Services Testing/Deployment for Pilot Courts	High/High	•Collaborate with Tyler to coordinate services deployment

Active Project Issues

Total Project Issues			
Active	Monitor	Deferred	Closed
0	0	0	0

Significant Issues Status

Issue	Urgency/Impact	Action

Next Steps

INH – Odyssey Integration	
Milestone	**Date**
Requirements Analysis - Complete	April 2014
Design - Complete	April 2014
Development - Complete	July 2014
Internal QA Testing - Complete	October 2014
UAT/Integration Testing With Odyssey - Complete	February 2015
Party Data Replication – Pilot Court Go Live	February 2015
