KING COUNTY DISTRICT COURT
CASE MANAGEMENT SYSTEM PROJECT UPDATE

Judge Donna Tucker – Presiding Judge

Othniel Palomino – Chief Administration Officer

KCDC
Updated: May 19, 2017

PROJECT OVERVIEW

Project Description

King County District Court is implementing a unified case management system using modern technology that would allow the Court to become more efficient and provide new services to the public. The primary objective of this implementation is to ensure public safety.

In Scope

- Core Case Management System
- eFiling
- Probation System Replacement
- Document Management System
- eMitigation System
- Digital Signatures
- Electronic Data Exchange – EDR
- External Interfaces not covered through Data Exchange
- Jury Management System

Out of Scope

- Video Conferencing Capabilities
- Court Audio Recording
- Interpreter Web
- Witness Management System
- Search Warrant Management System

PROJECT PHASES

- Phase 1 – August 2017
  - "Limited Civil" case types – Summons & Complaints, Judgment Summaries, Foreign Judgments, Collections – including Exparte Motions processing
  - New system for "Limited Civil" deployed to Burien, Issaquah, and Seattle locations
  - eFiling functionality
  - Public Portal

- Phase 2 – Spring 2018
  - "Full Civil" case types – Small Claims, Name Changes, Impounds, Protection Orders
  - New system for "Full Civil" deployed to all locations
  - Integration with the EDR

- Phase 3 – Summer 2018
  - "Criminal" & "Infraction" case types
  - New system for "Criminal" & "Infraction" deployed to all locations

RECENT & UPCOMING EVENTS

- "Limited Civil" operational/clerk power user session – 3/27 & 3/28 – **COMPLETE**
- "Limited Civil" judicial power user session – 3/29 & 3/30 – **COMPLETE**
- "Limited Civil" Training Coordinator training kick-off – 4/17 – **COMPLETE**
- Quarterly Ambassador Meeting – 4/18 – **COMPLETE**
- Quarterly Judge Meeting – 4/21 – **COMPLETE**
- Computer 'Word/Outlook/Internet' training – 4/11, 4/19, 4/28 – **COMPLETE**
- Computer 'Excel' training for managers – 5/3, 5/9, 5/11 – **COMPLETE**
- Training Content Development – 5/15 – 7/7 – **IN PROGRESS**
- Clerk & Manager Training – 7/10 – 8/11
- Judicial Training – 7/10 – 8/11

PROJECT HIGH-LEVEL TIMELINE - 2017

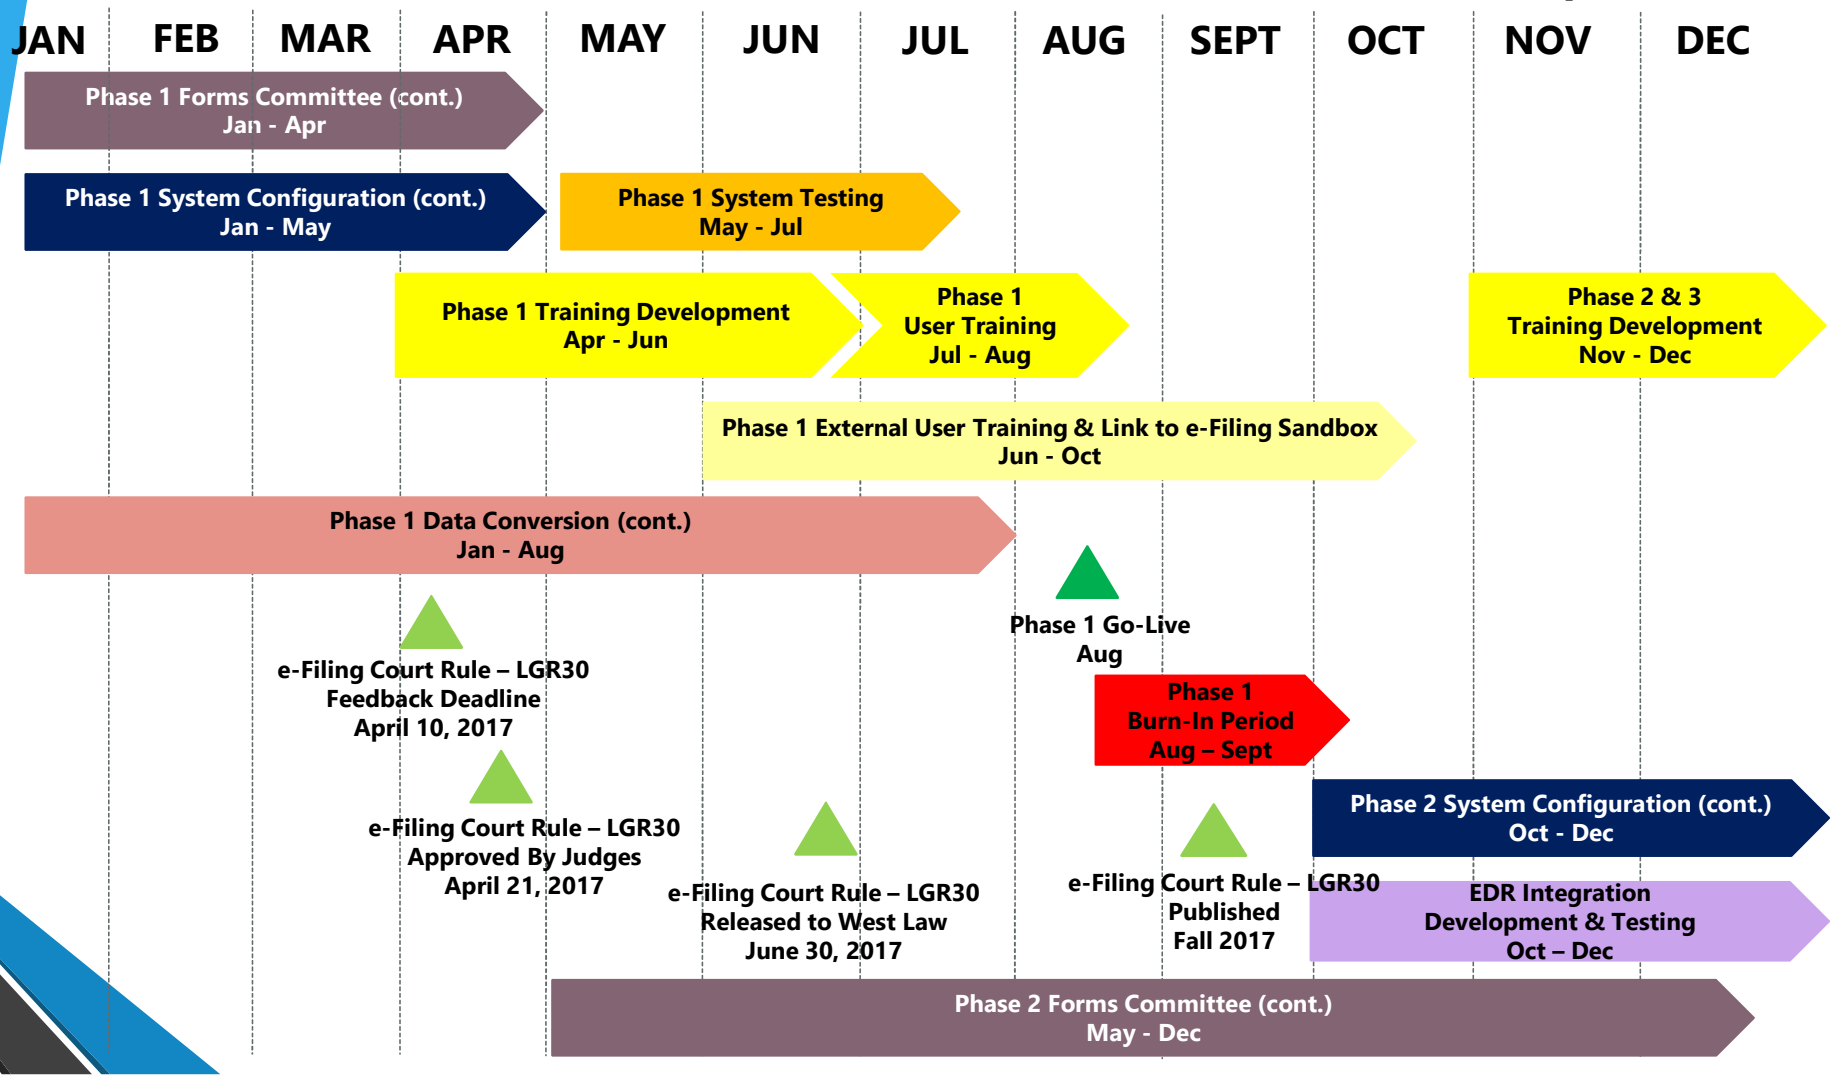

PROJECT HIGH-LEVEL TIMELINE - 2018

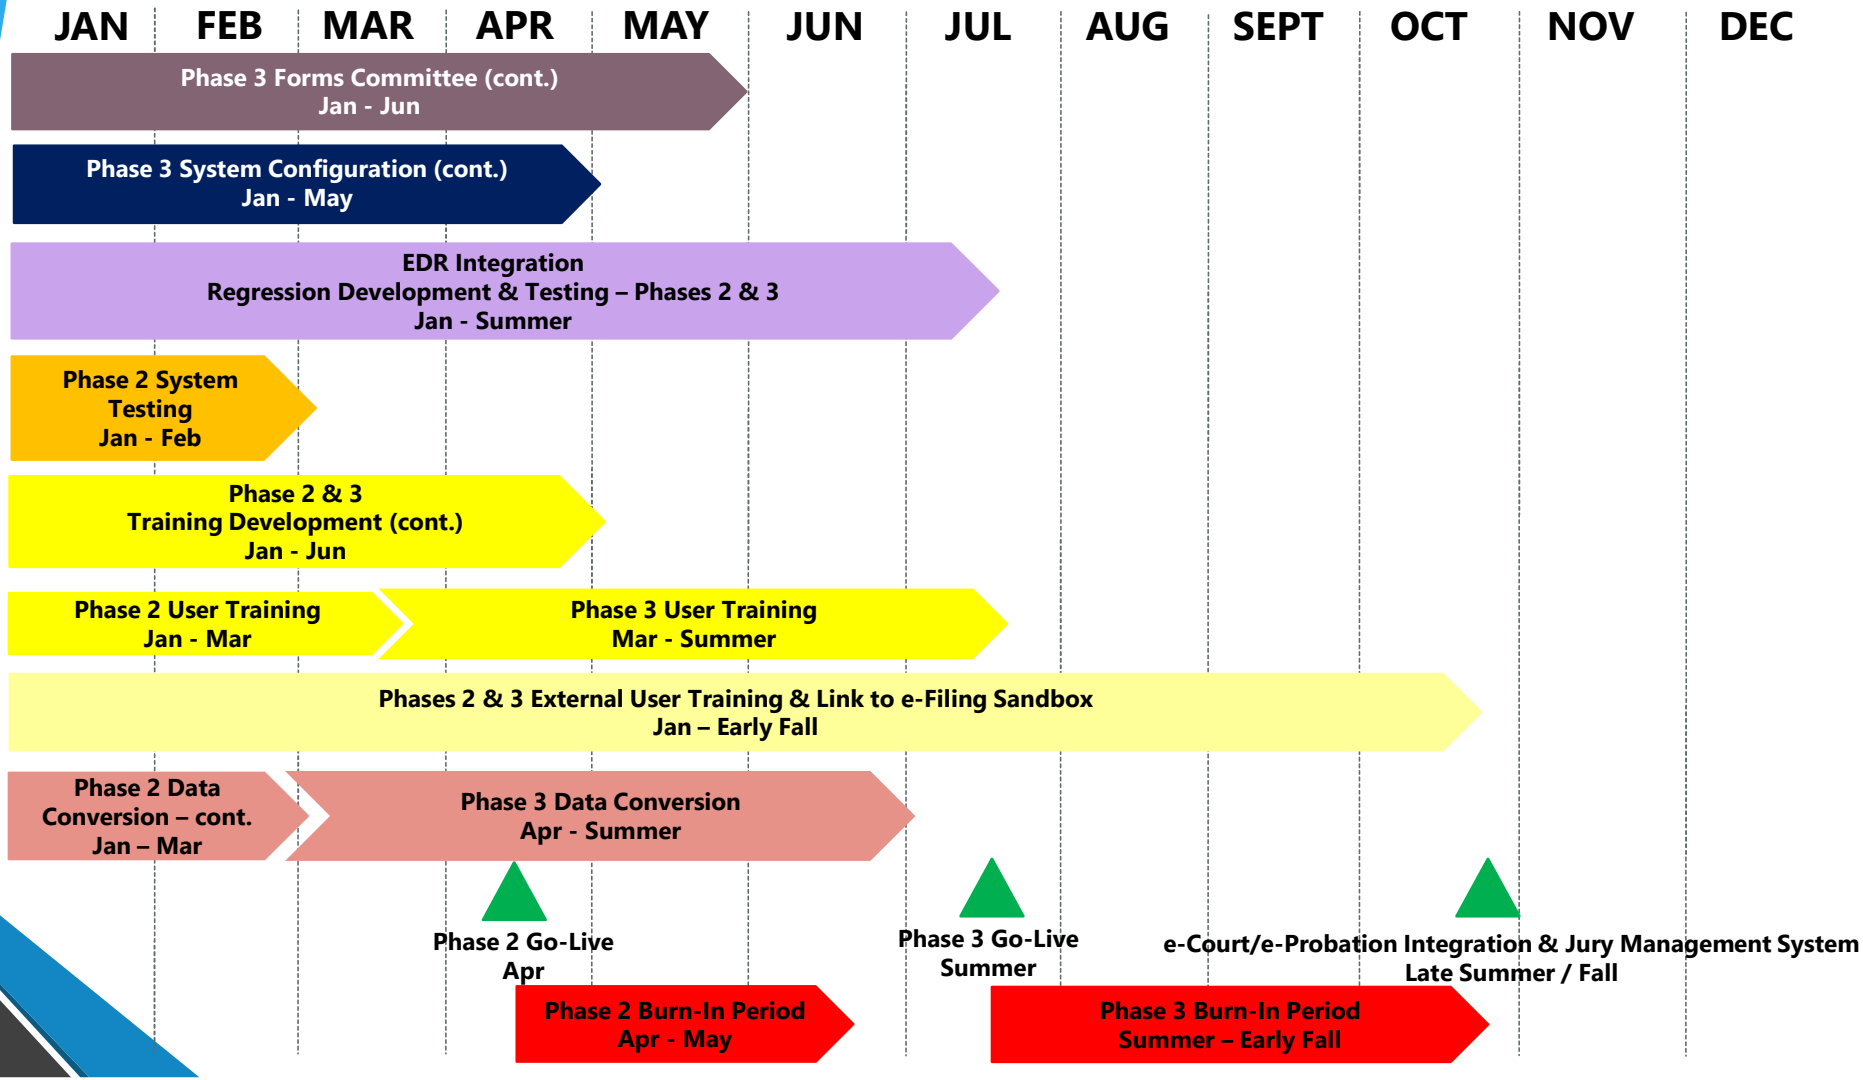

e-PROBATION PROJECT HIGH-LEVEL TIMELINE

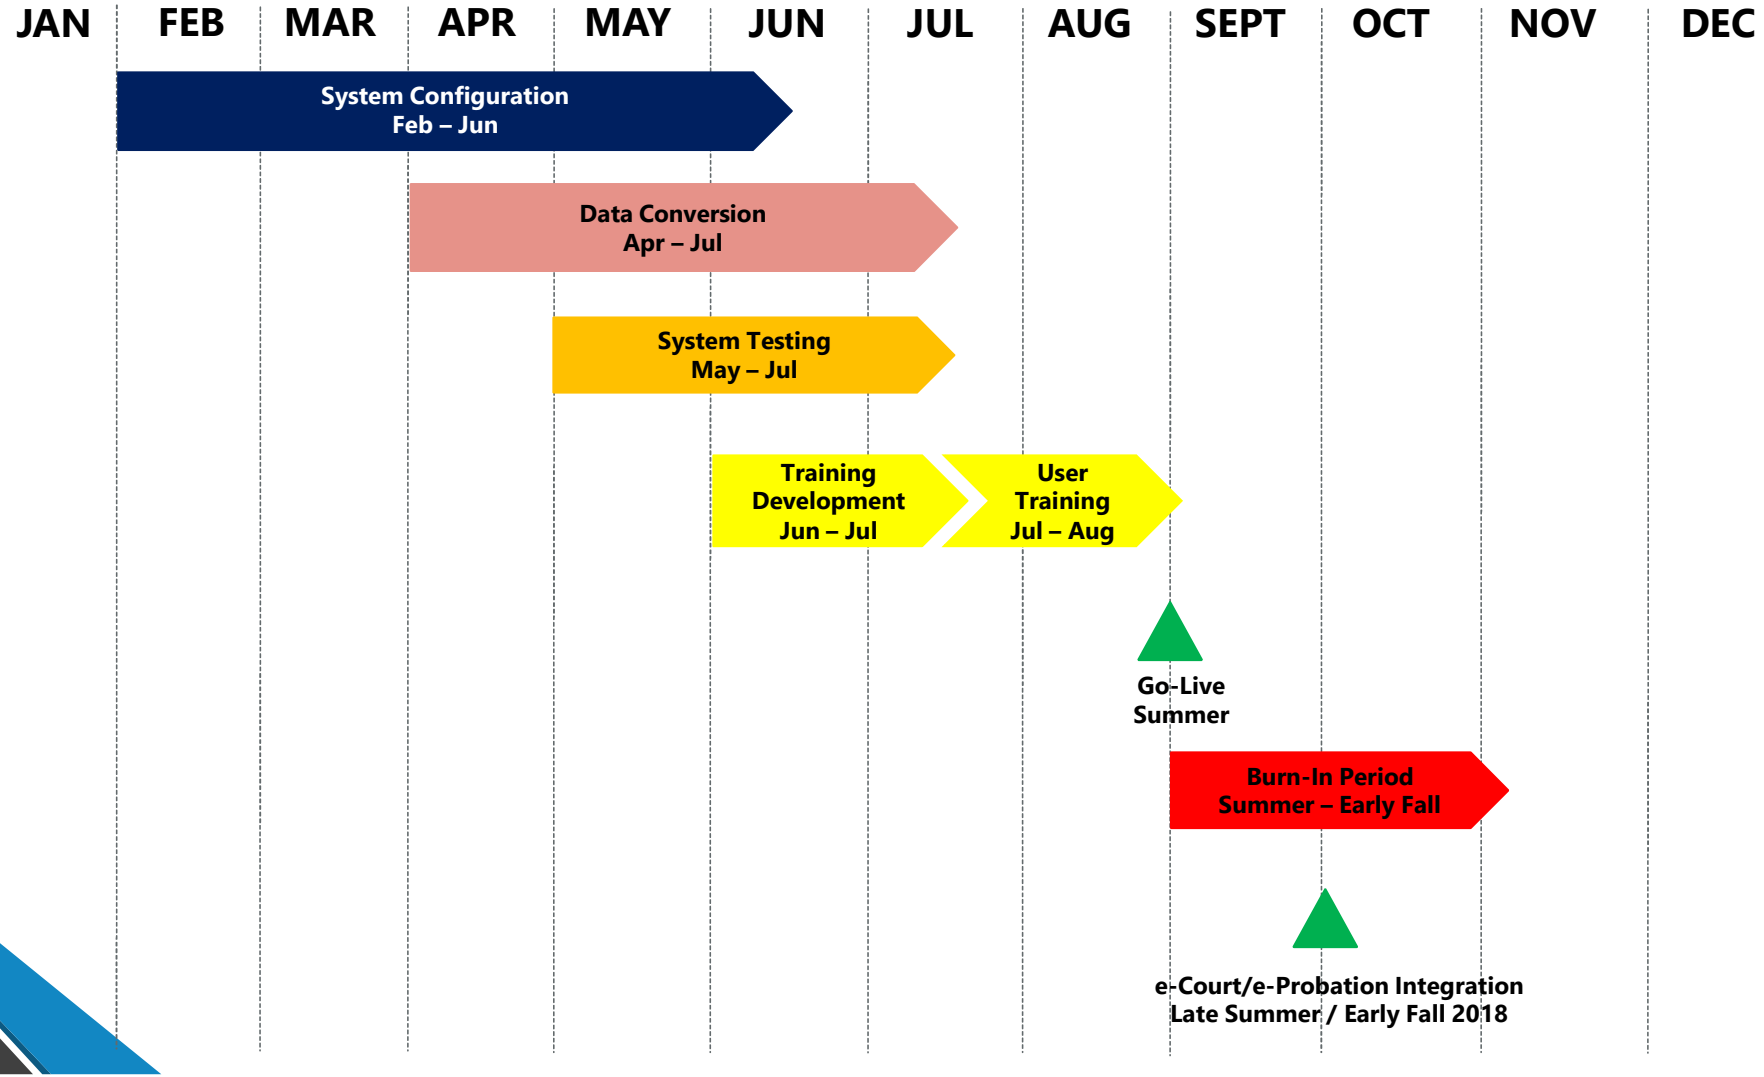

QUESTIONS?
