King County
District Court

KING COUNTY DISTRICT COURT
CASE MANAGEMENT SYSTEM PROJECT UPDATE

Judge Donna Tucker – Presiding Judge

Othniel Palomino – Chief Administration Officer

KCDC
Updated: October 10, 2018

PROJECT OVERVIEW

Project Description

King County District Court is implementing a unified case management system using modern technology that would allow the Court to become more efficient and provide new services to the public. The primary objective of this implementation is to ensure public safety.

In Scope

- Core Case Management System
- eFiling
- Probation System Replacement
- Document Management System
- eMitigation System
- Digital Signatures
- Electronic Data Exchange – EDR
- External Interfaces not covered through Data Exchange
- Jury Management System

Out of Scope

- Video Conferencing Capabilities
- Court Audio Recording
- Interpreter Web
- Witness Management System
- Search Warrant Management System

PROJECT PHASES

- Phase 1 – **DELIVERED**
  - Civil Phase 1 was successfully deployed to Production **October 30, 2017**
    - "Civil Phase 1" case types – Summons & Complaints, Judgment Summaries, Foreign Judgments, Collections – including Exparte Motions processing to Burien, Issaquah, and Seattle locations
    - eFiling functionality
    - Public Portal
  - eProbation module was successfully deployed to Production **October 9, 2017**

- Phase 2 – 1st Quarter 2019
  - "Civil Phase 2", "Criminal", and "Infraction" case types
  - All functionality deployed to all KCDC locations
  - eCourt and eProbation Integration
  - Integration with the EDR

RECENT & UPCOMING EVENTS

- Operational/Clerk Power User sessions – COMPLETED in July
- Workflow Configuration – Scheduled to COMPLETE in October
- Interface Development – IN PROGRESS
- Data Conversion Mapping – IN PROGRESS
- User Training Plan Development – Scheduled to COMPLETE in October
- End-to-End Testing – Scheduled to START in November
- User Training Content/Material Development – Scheduled to START in November
- User Training – Scheduled to START in January 2019
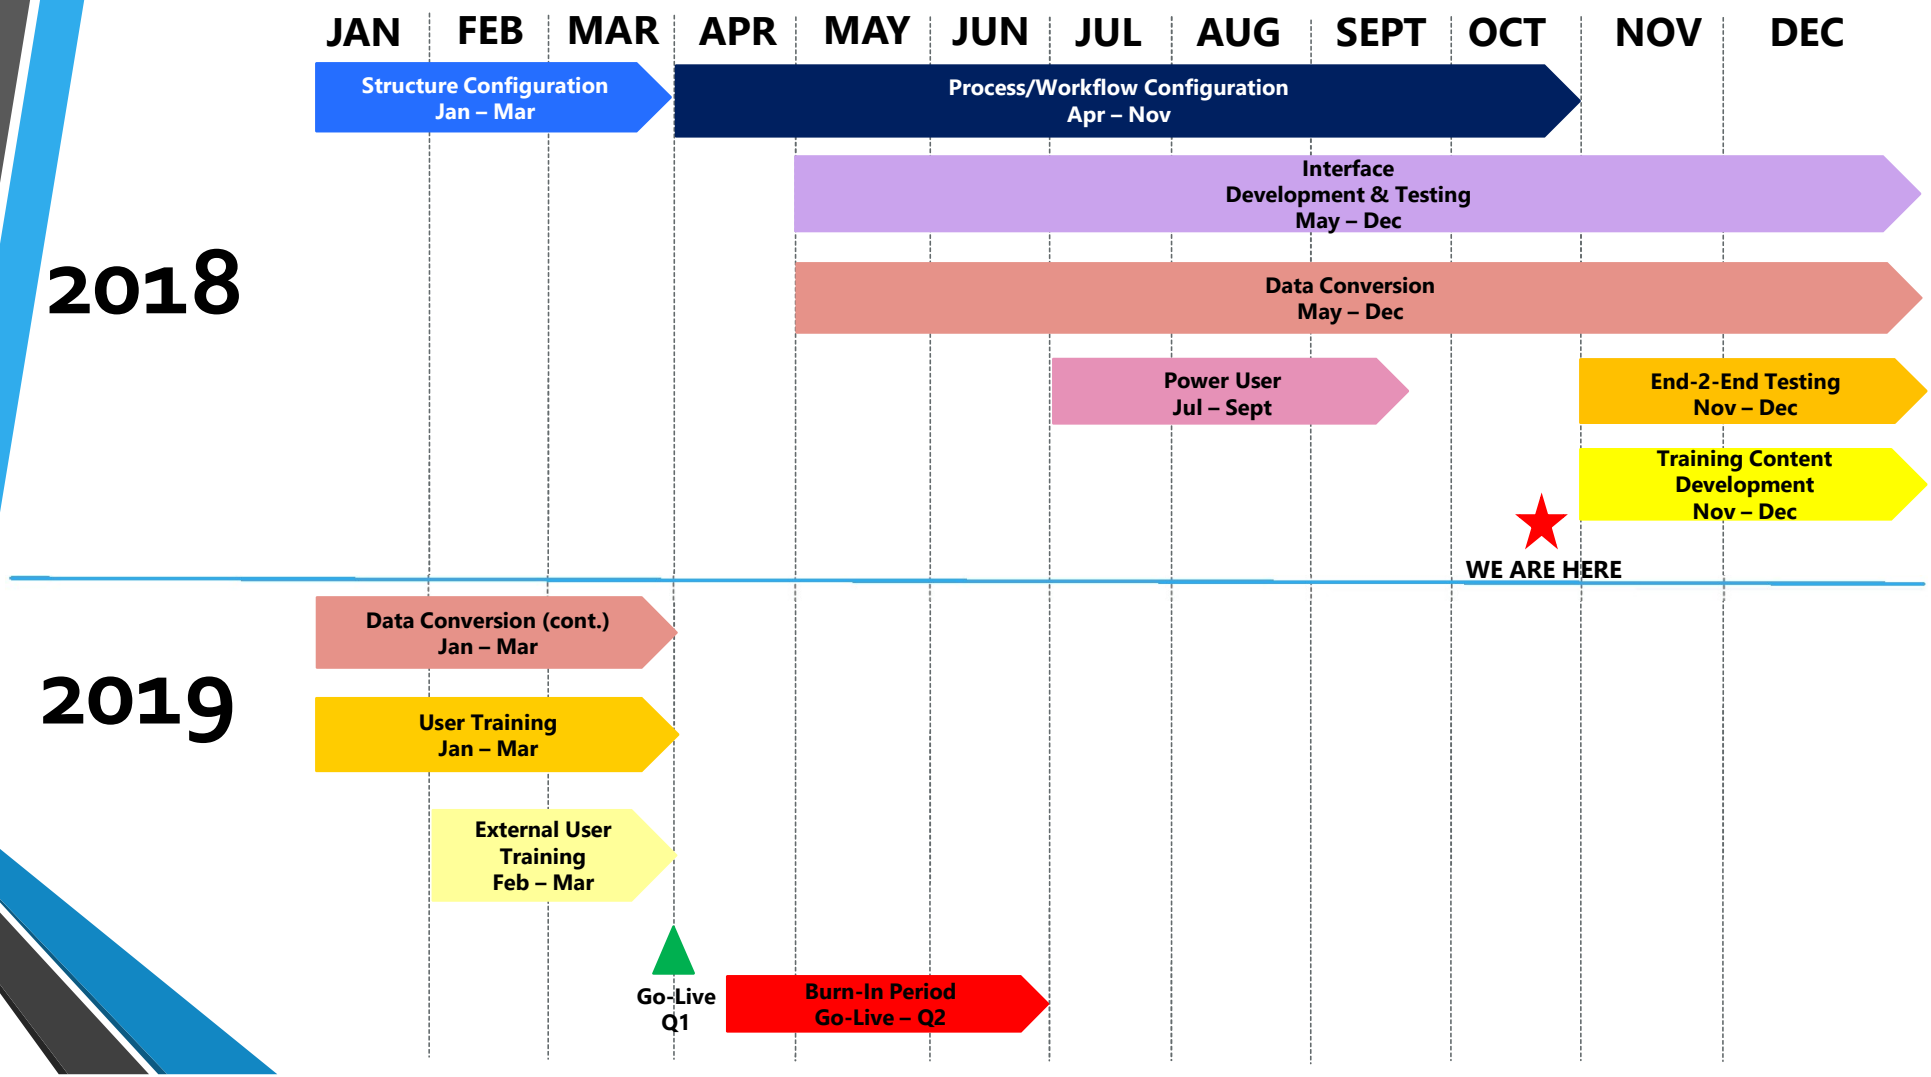
DRAFT - PROJECT HIGH-LEVEL TIMELINE
