Vehicle Related Violations (VRV) Status Update

October 20, 2011

VRV Tier 1 Current Status

- The JINDEX Release 1 implementation is falling behind schedule.
- Weekly project stand up meetings have been scheduled to help step up the pace.
- The VRV Tier 1 pilot courts, Lakewood, Kirkland, and Issaquah, are in the process of connecting and testing their web services with JINDEX
- The current release schedule has the three courts targeted for a November 4th production date.

Release One – VRV
Version: 2-re-baseline

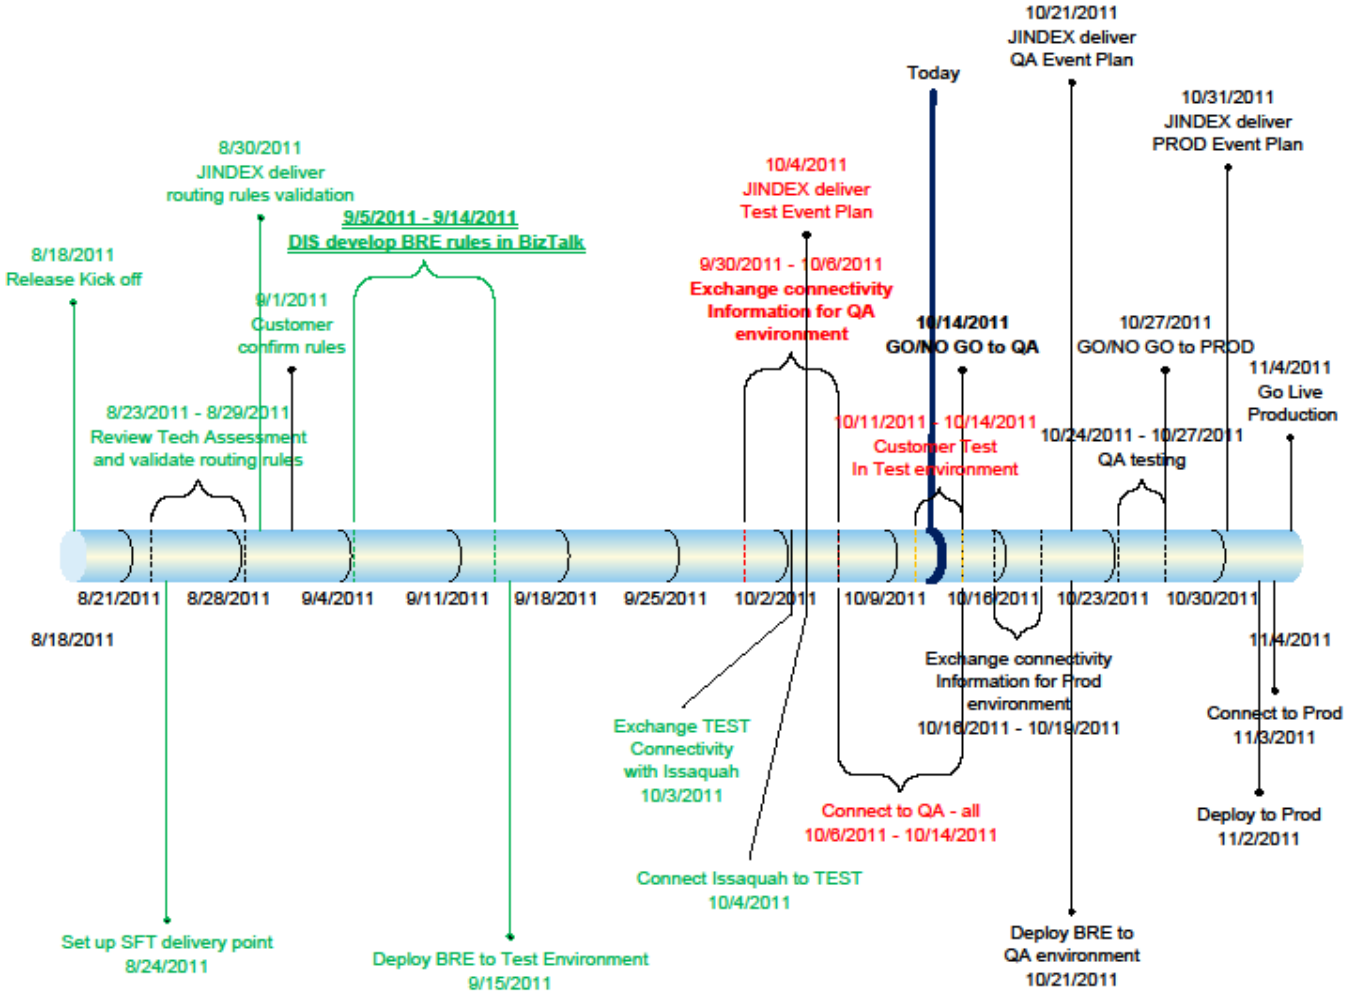

Tier 1 Next Steps

- AOC is putting together a functional test plan to verify that the VRV message will process properly.
- The functional/acceptance testing will start at the completion of the JINDEX Release 1 move to production

Delays and schedule changes

- DIS acknowledged that they underestimated the complexity involved in on-boarding our courts.
- As a result, this has been and continues to be a learning processes for all involved.
- DIS has implemented a release management schedule that provides only one release per quarter.
- It is expected that as we gain more knowledge and experience the process with eventually smooth itself out.

Release One - Target Schedule

Fiscal Year 2011 – 2012
JINDEX Target Release Schedule

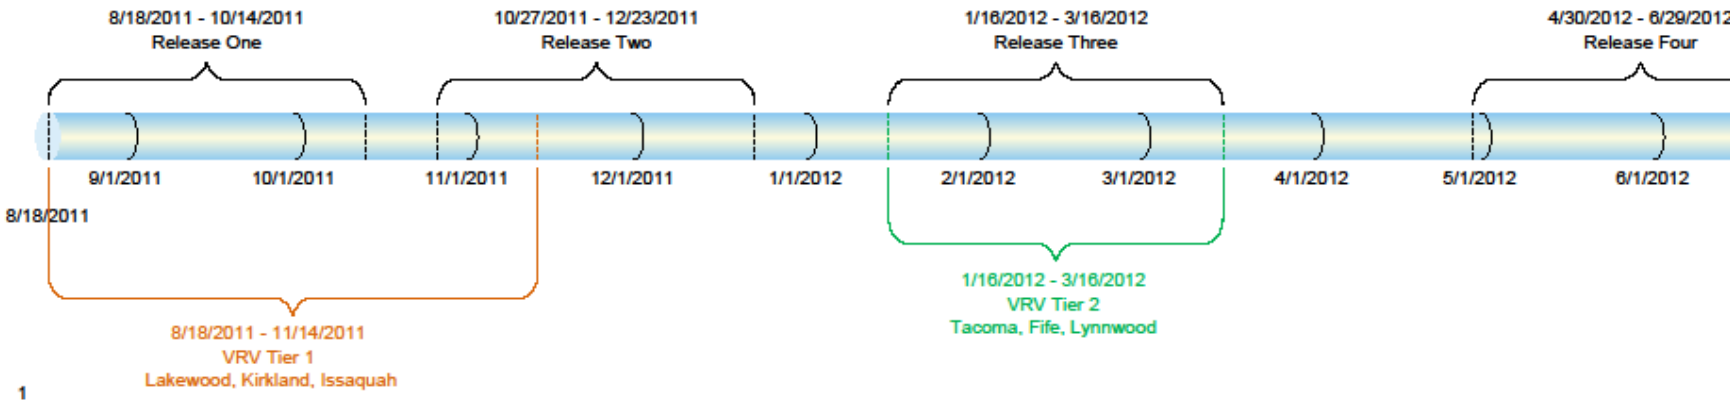

VRV Tier 2 update

- Tier 2 courts (Fife, Tacoma, and Lynnwood) are now slotted for inclusion in the JINDEX Jan – Mar 2012 release group 3.
- The ATS and Redflex web services, created for the Tier 1 courts, will be used the Tier 2 courts.
- This will cut down on the time and effort needed to implement the VRV solutions for Tier 2 and all other future business partners.

Tier 2 on boarding strategy

- As we roll off the Tier 1 implementation, AOC will start bi-weekly meetings of the Tier 2 work group.
- We will use these meetings to leverage the lessons learned from the first group of courts.
- We will use the same method of collaboration and coordination used successfully with the Issaquah, Kirkland, and Lakewood.
