# Vehicle Related Violations (VRV) Status Update

March 4, 2011

# eTRIP Initiative

Electronic Traffic Information Processing Initiative

- The eTRIP initiative is a collaborative effort among state and local agencies to create a seamless and integrated system through which traffic-related information can travel from its point of origin to its end use and analysis
- http://trafficrecords.wa.gov/eTRIP/eTRIP_Default.aspx

# eTRIP System Components

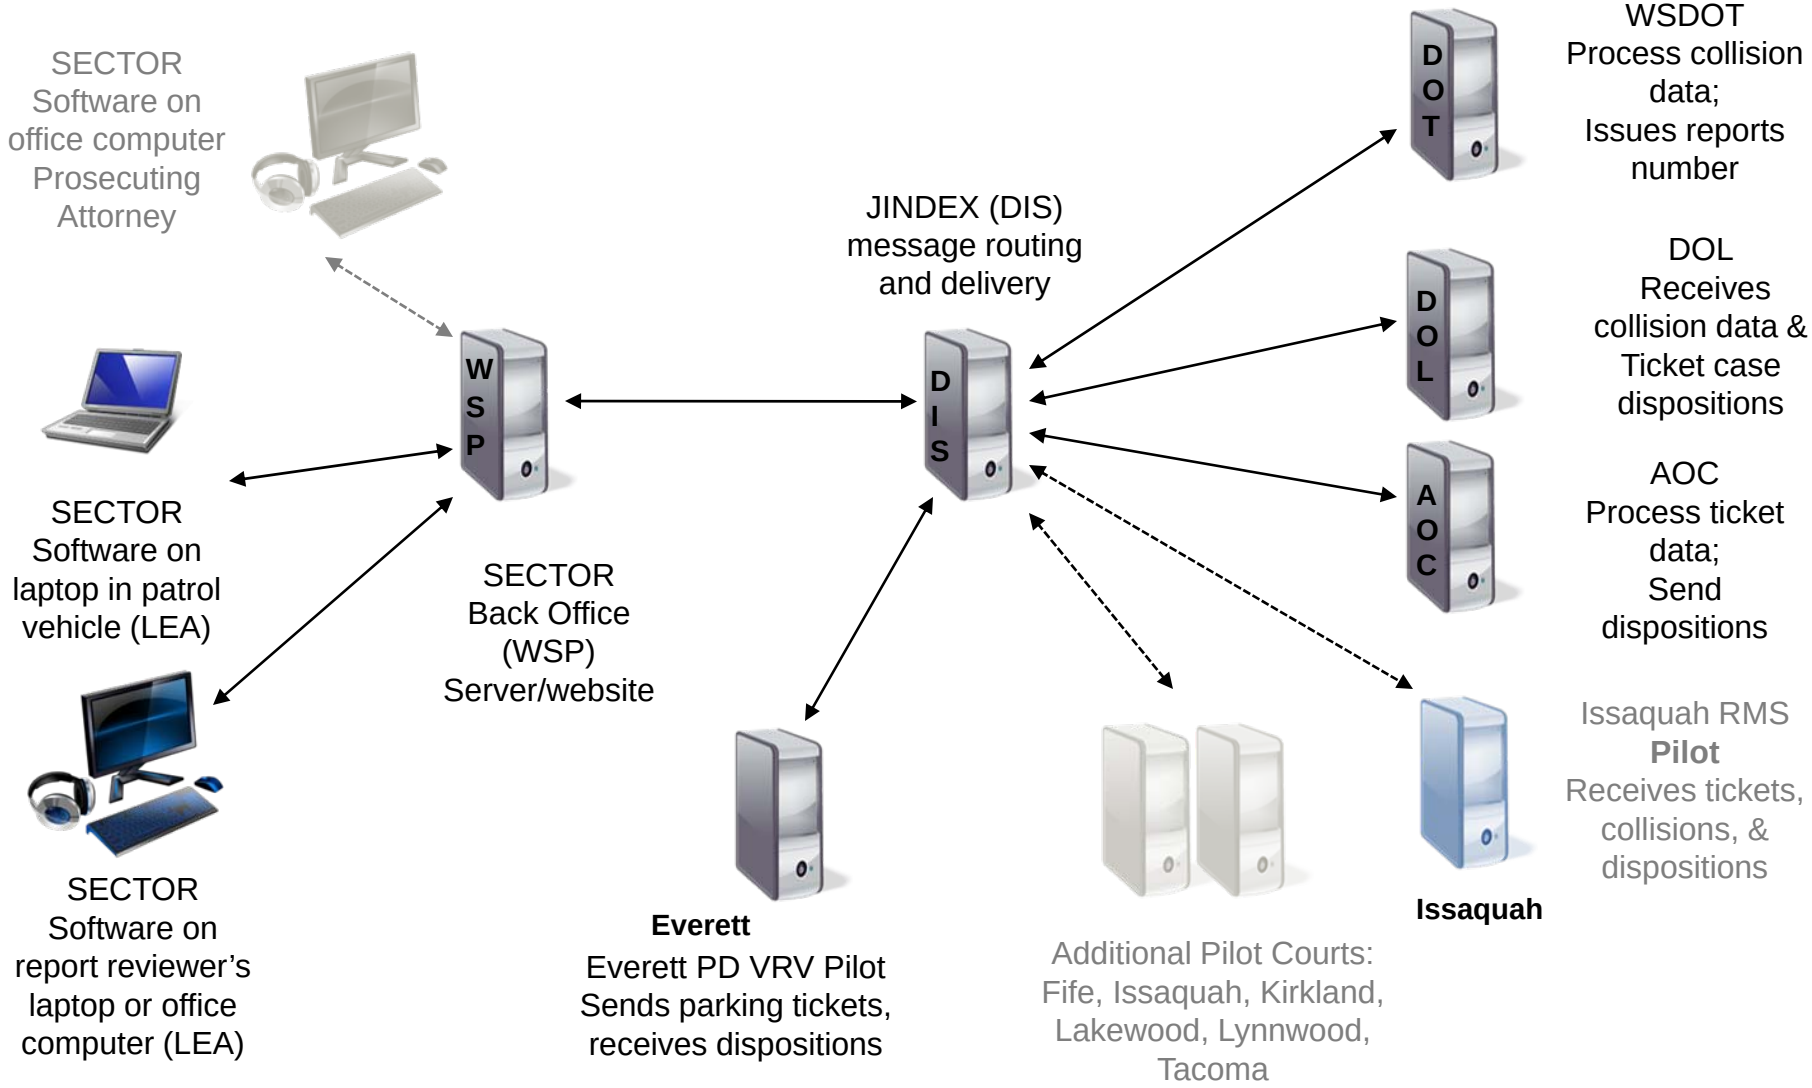

# eTRIP Challenges

- Non-traditional project.
  - Monitoring and control.
- Complex solution relies on cooperation and coordination of multiple agencies.
- Each agency has some technical responsibility.
- No one agency has authority/oversight over another.
- Data is exchanged using a common message protocol.

# Record Management System (RMS) issues affecting VRV

- Challenges coordinating testing with multiple agencies.
- Schedule delays have been escalated and are being addressed.
- Revised RMS Go-Live target date is late April 2011.
  - Two months of system stabilization required.
  - No new changes during this time frame.
- Issue with the sequencing of the RMS on boarding process may impact the VRV on-boarding schedule.
- VRV courts on-boarding is ***tentatively*** planned for July 2011.

# VRV Current Status

- Operational readiness project code changes implemented.
- Sent communication to all on-boarding courts describing current status and projected implementation dates.
- Revisions to VRV data exchange web portal in process.
- On-going support responsibility transitioning to maintenance teams.

# Next steps

- Continue to communicate data exchange status and specification changes to pilot courts and their technical partners.
- Transition VRV support to maintenance teams.
- Continue to monitor the RMS schedule delays and investigate alternatives.
