Superior Court Data Exchange Project Status

June 22, 2012

Superior Court Data Exchange Project

Increment 1 Status:

✓ Development completed.

- QA Team continuing to test SCDX Increment 1:
  - 70% of testing has been completed.
  - Identified (12) non-critical defects.
- Testing is taking significantly longer than expected due to availability of QA resources and more time required to perform these tests:
  - Additional Testers will be added to the effort.
  - AOC QA Test Manager expects to complete testing of Increment 1 by June 29.

Superior Court Data Exchange Project

Increments 2 & 3 Status:

- ✓ Increment 2 development completed June 11.
- Increment 2 QA testing scheduled to begin in July.
- Increment 3 development in-work and scheduled to be completed in August.

Superior Court Data Exchange Project Schedule

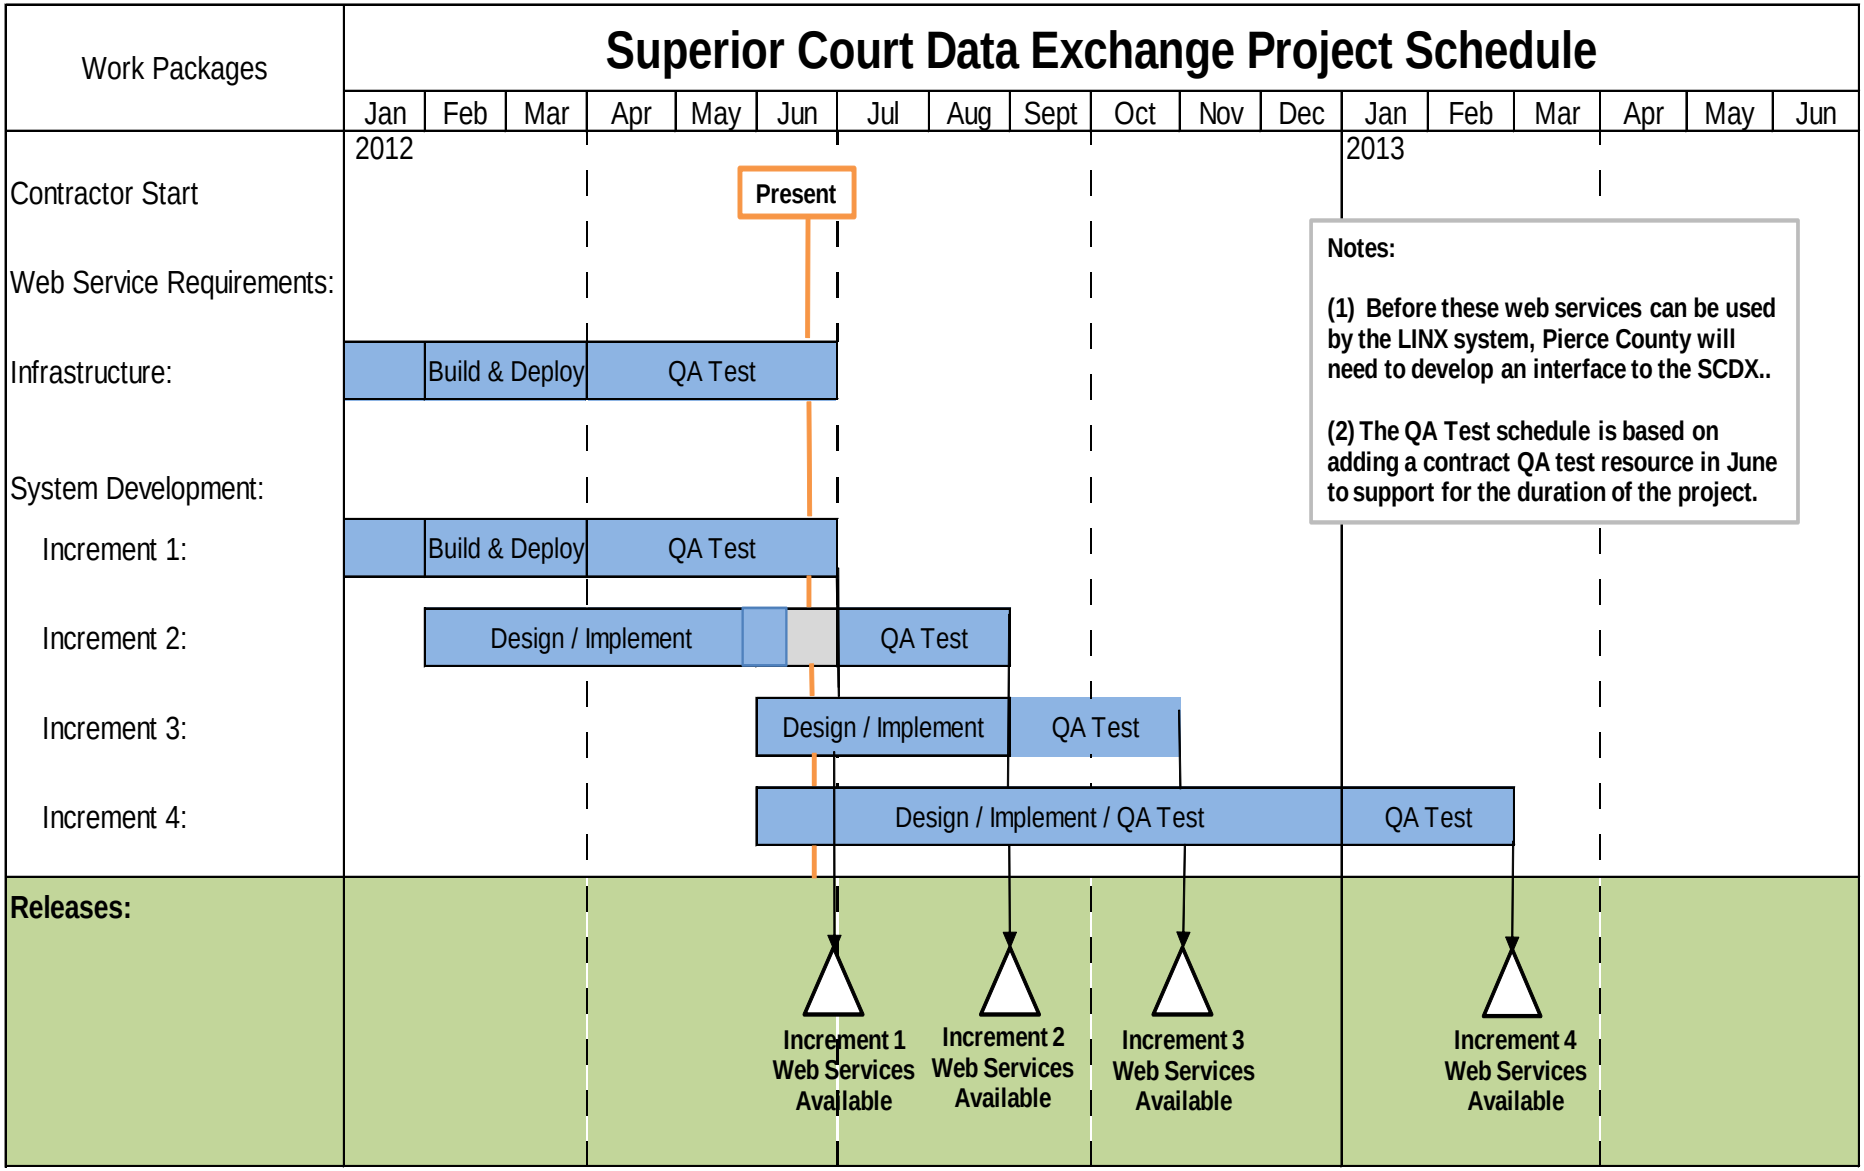

Superior Court Data Exchange Project

Increment 4 Planning:

- AOC will develop (13) SCDX web services:
  - Training opportunity for AOC Developers.
  - Reduces the cost for SCDX Increment 4.
  - Will complete this development by December.
- Sierra Systems has submitted a proposal for developing the remaining (12) SCDX Increment 4 web services:
  - Firm Fixed Price – TBD, awaiting vendor response
- JISC is requested to approve SCDX Increment 4 funding allocation required for Sierra Systems development.

Superior Court Data Exchange Project
High-Level Architecture

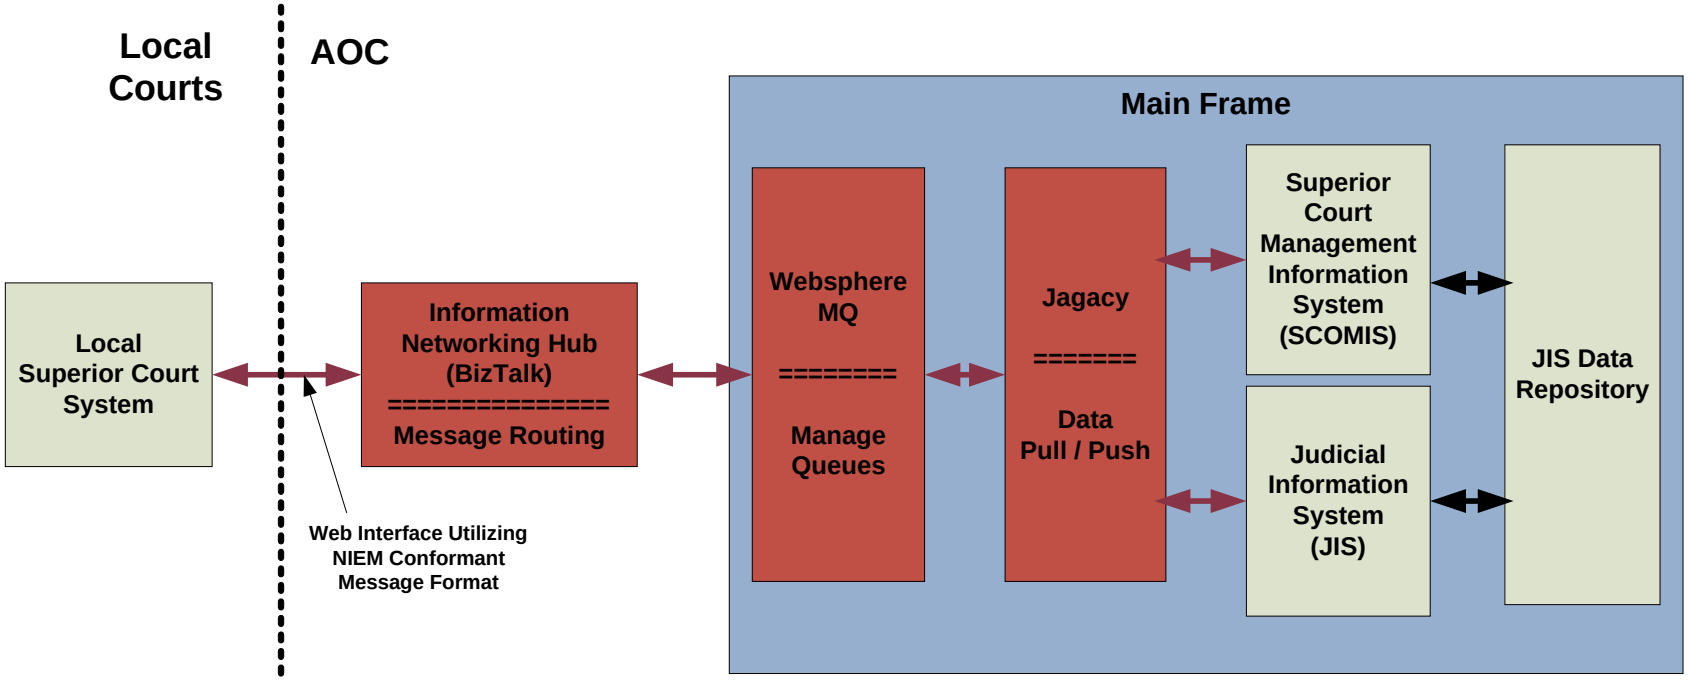



- Color denotes areas of SCDX project development
