Superior Court Data Exchange

Project Status

Mike Walsh, Project Manager

October 26, 2012

Superior Court Data Exchange Project

Increment 1 Status:

✓ 10 Web Services are ready for Production data.

- AOC project team is assisting Pierce County in their web services implementation.
- Pierce County can start sending real transactions once their QA testing and verification is complete.

❑ SCDX technical documentation is available at the following URL:

- http://dx.courts.wa.gov/

Superior Court Data Exchange Project

WASHINGTON COURTS

Data Services Home | eService Center

Washington Courts Data Services Portal

Welcome to the Information Services Division Data Services Portal, where you can get the latest information on new integration service offerings, technical details for implementation, and answers to frequently asked questions. This web portal is intended for current and potential users of Washington Court Data Services (data exchange/web services), who have a need to exchange information with the Administrative Office of the Courts (AOC).

The AOC on behalf of the Washington Courts is committed to delivering data services that enable a consistent, defined set of standards and a standard technology solution for sharing data between Judicial Information System (JIS) applications supported by the AOC, the Courts and their judicial partners.

As data services are developed and made available, the business and technical documentation for using them will be posted and maintained here.

DX DATAEXCHANGE

Watch the Demo

Courts of Limited Jurisdiction

- CLJ Service Catalog

VRV Overview: Business, Technical | Service Level Agreement

Superior Courts

- Superior Court Service Catalog

Service Level Agreement

Washington Courts Website | Inside Courts Website | Contact Us

Superior Court Data Exchange Project

Increment 2 Status:

- ✓ Test tool delivered and is being applied for testing.
  - Significant gains in test execution and results gathering.
- ❑ Project is continuing to experience challenges with test resources, both contractor and staff.
  - Test case preparation is taking significantly longer than planned.
- ❑ QA Testing is six weeks behind schedule and is targeted for a December 2012 completion.

Superior Court Data Exchange Project

Increment 3 Status:

- ✓ All twelve web services were delivered by Aug. 3, 2012.
- ❑ QA Testing is delayed and targeted for a November 2012 start.
- ❑ QA Testing is targeted for a February 2013 completion.

Superior Court Data Exchange Project

Increment 4:

- All twenty five web services scheduled to be delivered by end of November 2012.
  - ✓ Sierra delivered all twelve web services by October 3, 2012.
    - ➢ Sierra delivered 3 weeks ahead of schedule.
  - Thirteen web services assigned to AOC Staff.
    - ✓ Seven web services have been developed.
    - ➢ Development is on schedule.
  - QA Testing is delayed and targeted for a January 2013 start.
  - QA Testing targeted for a July 2013 completion.

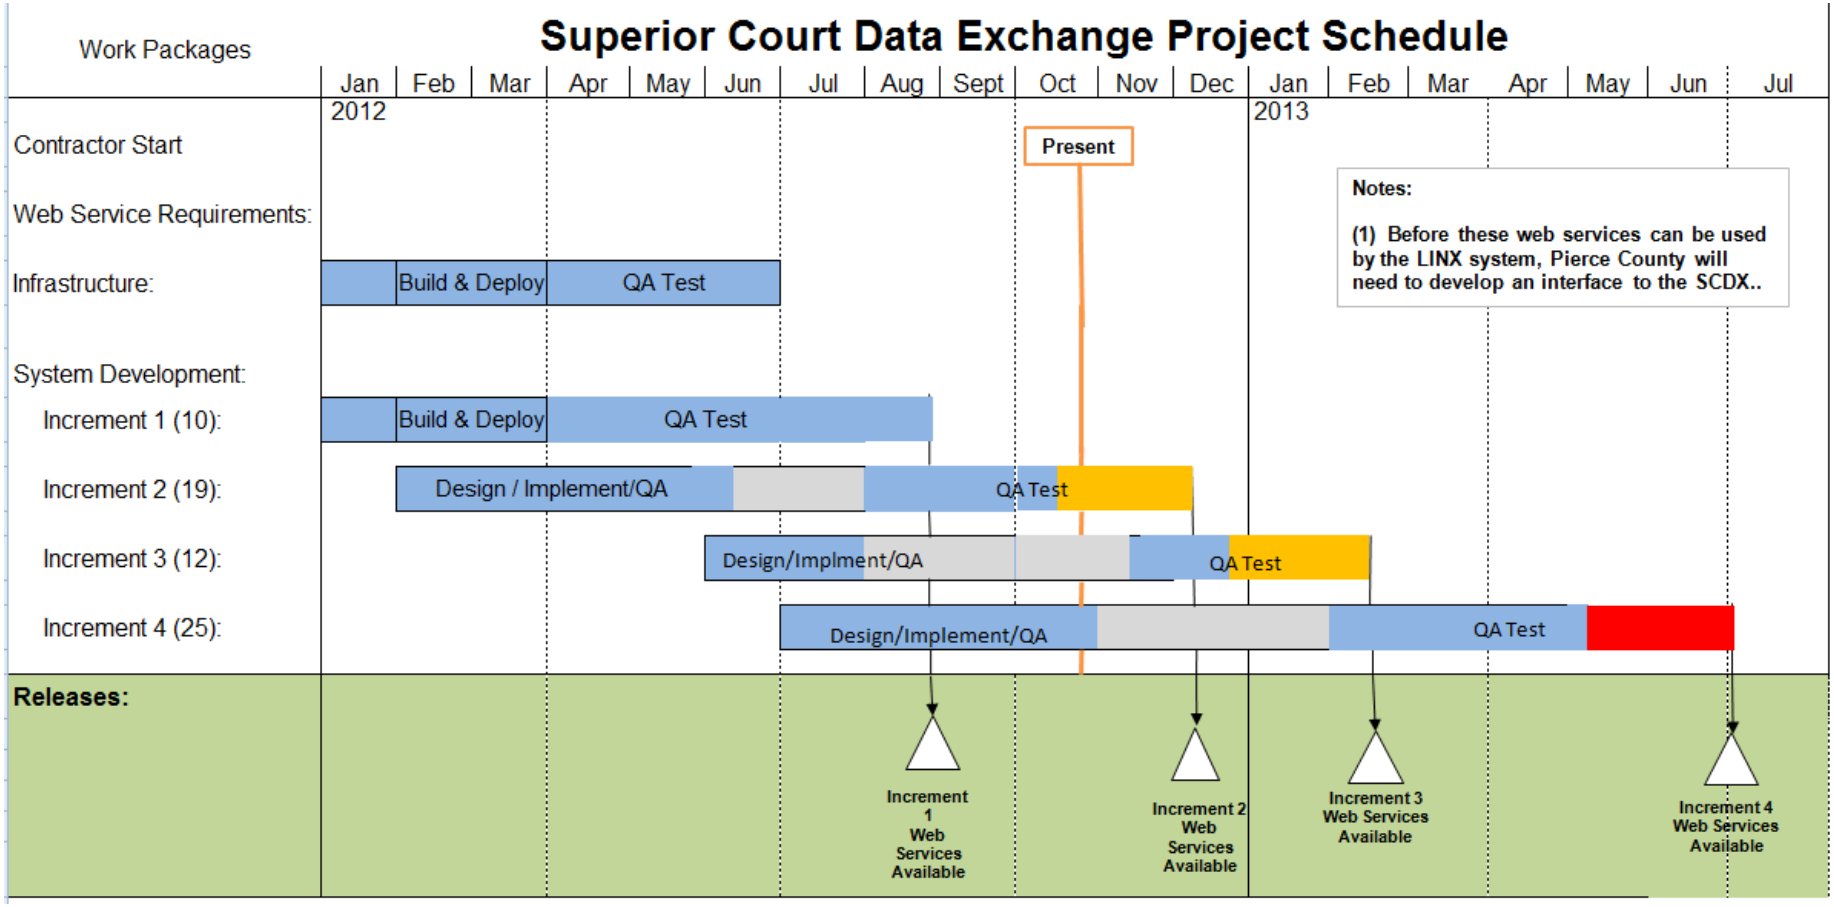
Superior Court Data Exchange Project Schedule
Work Packages
Jan Feb Mar Apr May Jun Jul Aug Sept Oct Nov Dec Jan Feb Mar Apr May Jun Jul
2012
2013
Contractor Start
Present
Web Service Requirements:
Notes:
(1) Before these web services can be used by the LINX system, Pierce County will need to develop an interface to the SCDX..
Infrastructure:
Build & Deploy
QA Test
System Development:
Increment 1 (10):
Build & Deploy
QA Test
Increment 2 (19):
Design / Implement/QA
QA Test
Increment 3 (12):
Design/Implment/QA
QA Test
Increment 4 (25):
Design/Implement/QA
QA Test
Releases:
Increment 1 Web Services Available
Increment 2 Web Services Available
Increment 3 Web Services Available
Increment 4 Web Services Available

Active Project Issues

Total Project Issues			
Low Urgency	Medium Urgency	High Urgency	Closed
0	0	1	0

High Urgency Issues Status

Issue	Category	Action
Test turn around impacting schedule	High/High	• Added two contract testers, lost one • Acquired test tool from Sierra Systems • Revised testing methods • Grouped test assignments • Improved test planning • Reviewing test coverage options •Reviewing resource assignments

Superior Court Data Exchange Project High-Level Architecture

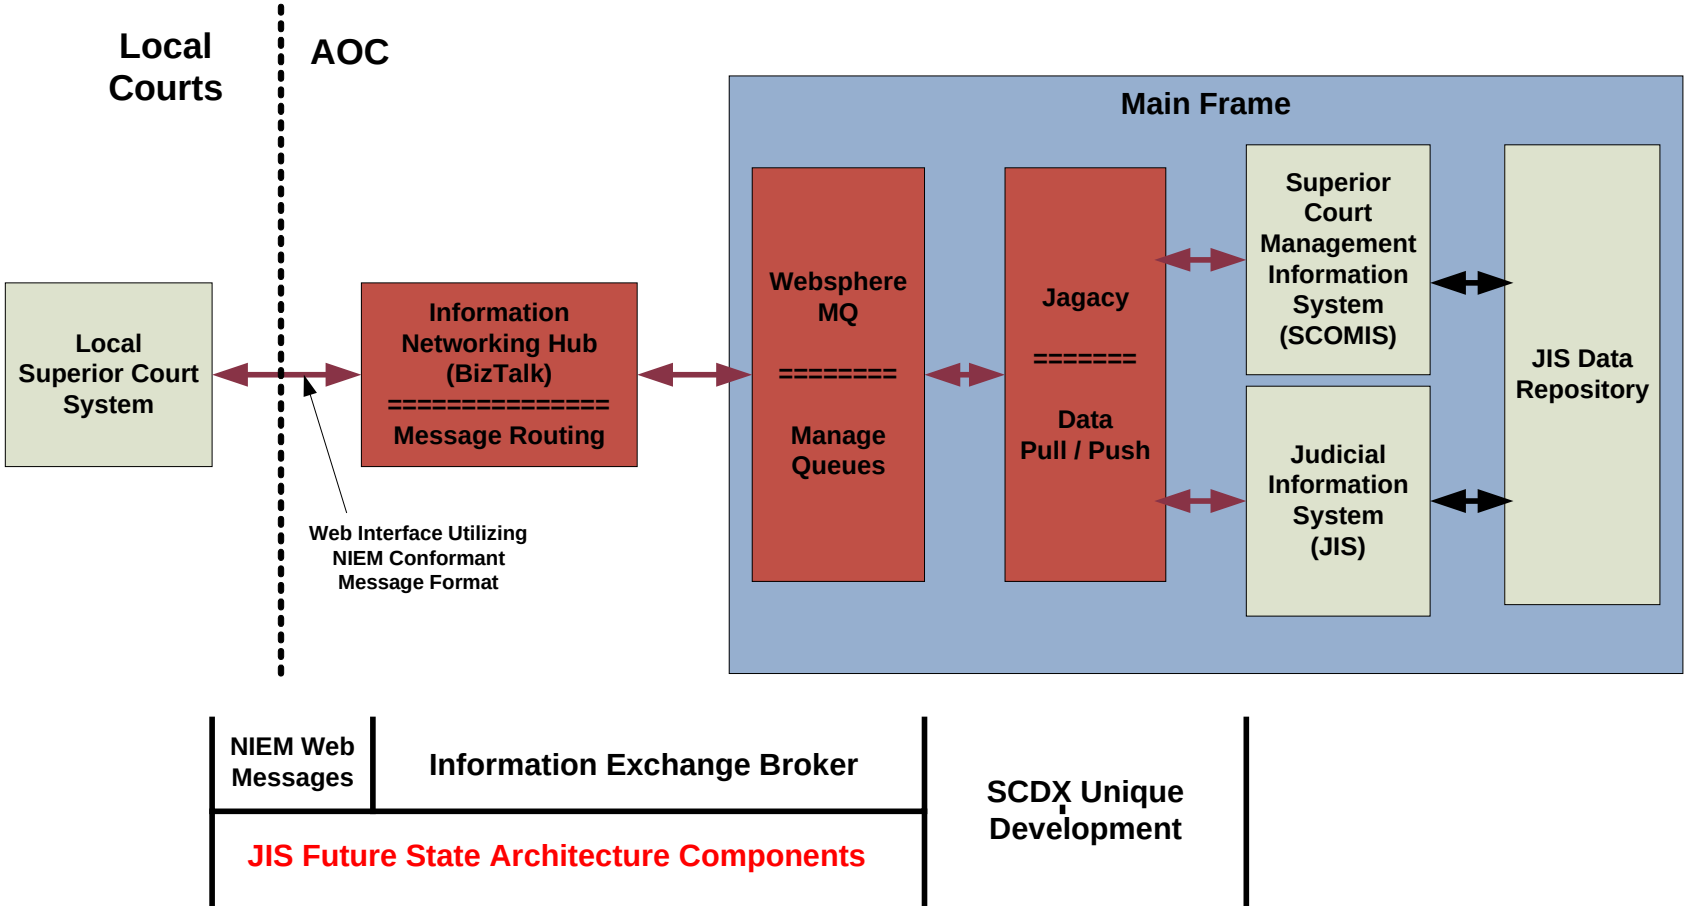

- Color denotes areas of SCDX project development
