Superior Court Data Exchange

Project Update

Mike Walsh, Project Manager

April 26, 2013

Recent Activities

Increment 1 Status (10 web services):

- Problem discovered in docket service validation: Pierce County docket entries when submitted out of file date order, may create an incorrect case status in SCOMIS
  - ❑ Corrections and testing of the program changes are in progress
- Pierce County will continue to validate other web services as planned

Increment 2 Status (19 web services)

✓ All 19 services are ready for Pierce County to start validating

Recent Activities

Increment 3 Status (12 web services)

- ✓ All services have passed testing
- ❑ Awaiting approval and deployment

Increment 4 Status (25 web services)

- ✓ 12 of 25 services have passed testing
- ❑ Awaiting approval and deployment
- ❑ The remaining 13 services are in first round testing

Schedule

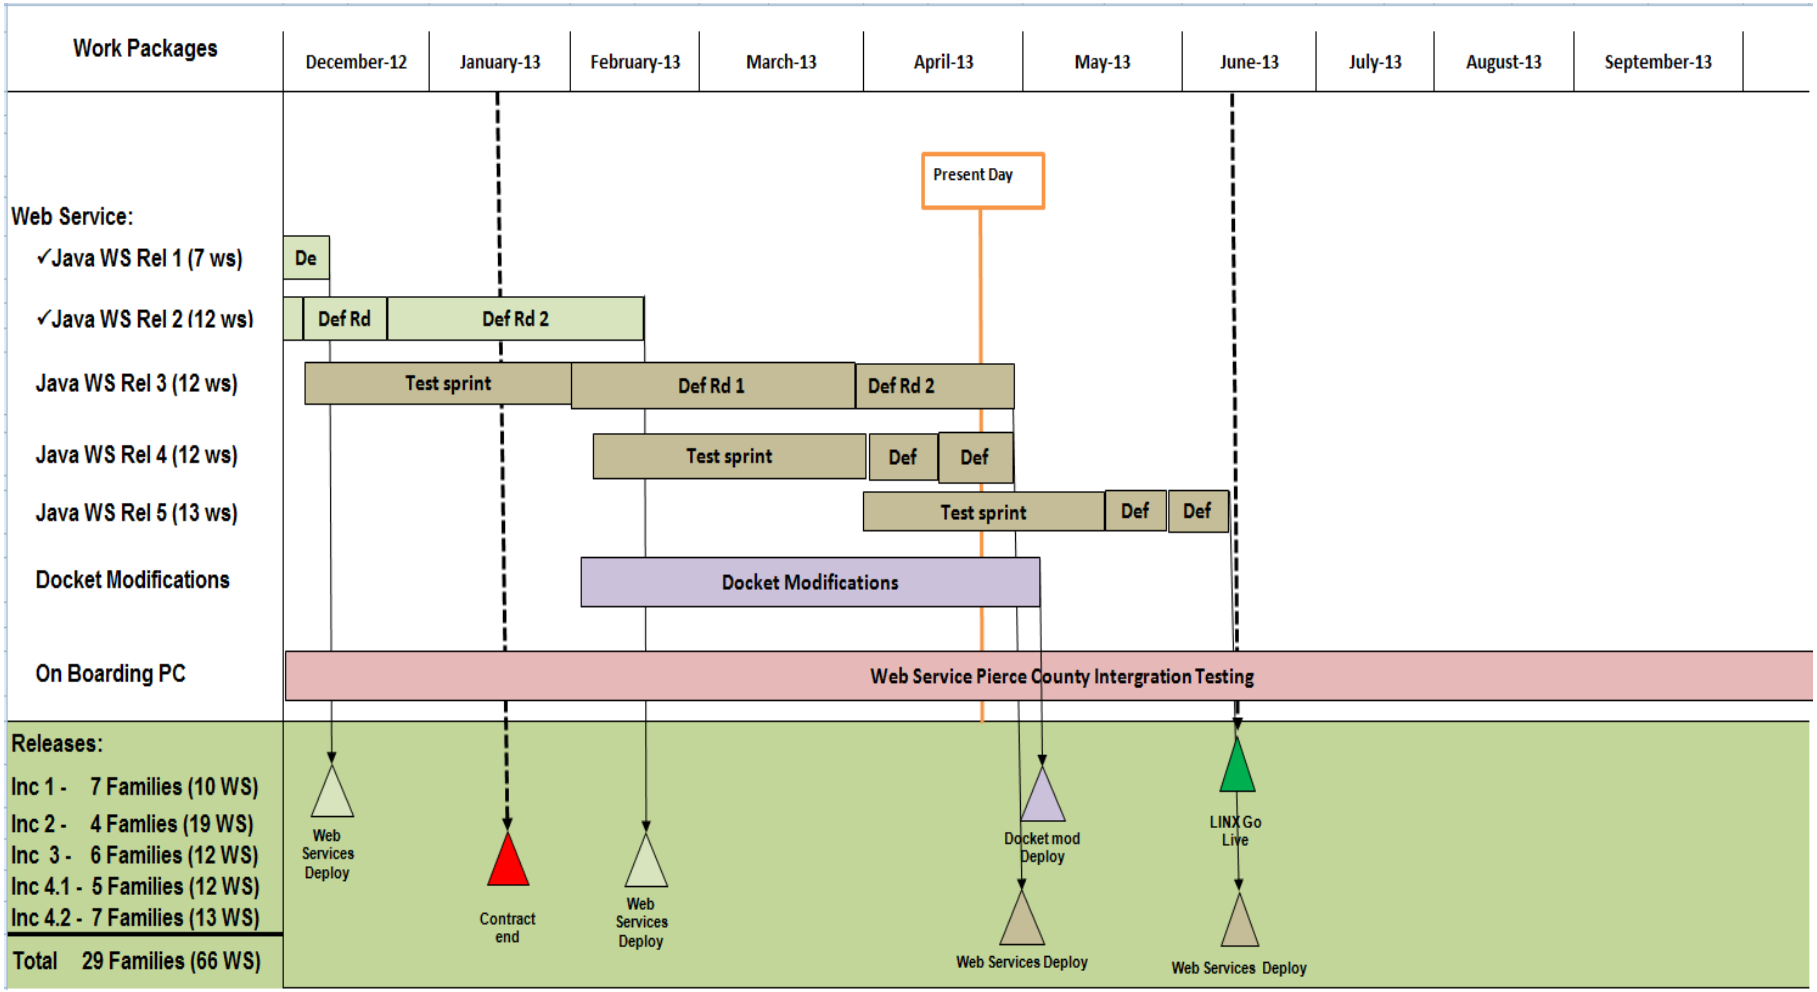
Work Packages
December-12
January-13
February-13
March-13
April-13
May-13
June-13
July-13
August-13
September-13
Present Day
Web Service:
✓Java WS Rel 1 (7 ws)
De
✓Java WS Rel 2 (12 ws)
Def Rd
Def Rd 2
Java WS Rel 3 (12 ws)
Test sprint
Def Rd 1
Def Rd 2
Java WS Rel 4 (12 ws)
Test sprint
Def
Def
Java WS Rel 5 (13 ws)
Test sprint
Def
Def
Docket Modifications
Docket Modifications
On Boarding PC
Web Service Pierce County Intergration Testing
Releases:
Inc 1 - 7 Families (10 WS)
Inc 2 - 4 Famlies (19 WS)
Inc 3 - 6 Families (12 WS)
Inc 4.1 - 5 Families (12 WS)
Inc 4.2 - 7 Families (13 WS)
Total 29 Families (66 WS)
Web Services Deploy
Contract end
Web Services Deploy
Docket mod Deploy
Web Services Deploy
LINX Go Live
Web Services Deploy

When are we done?

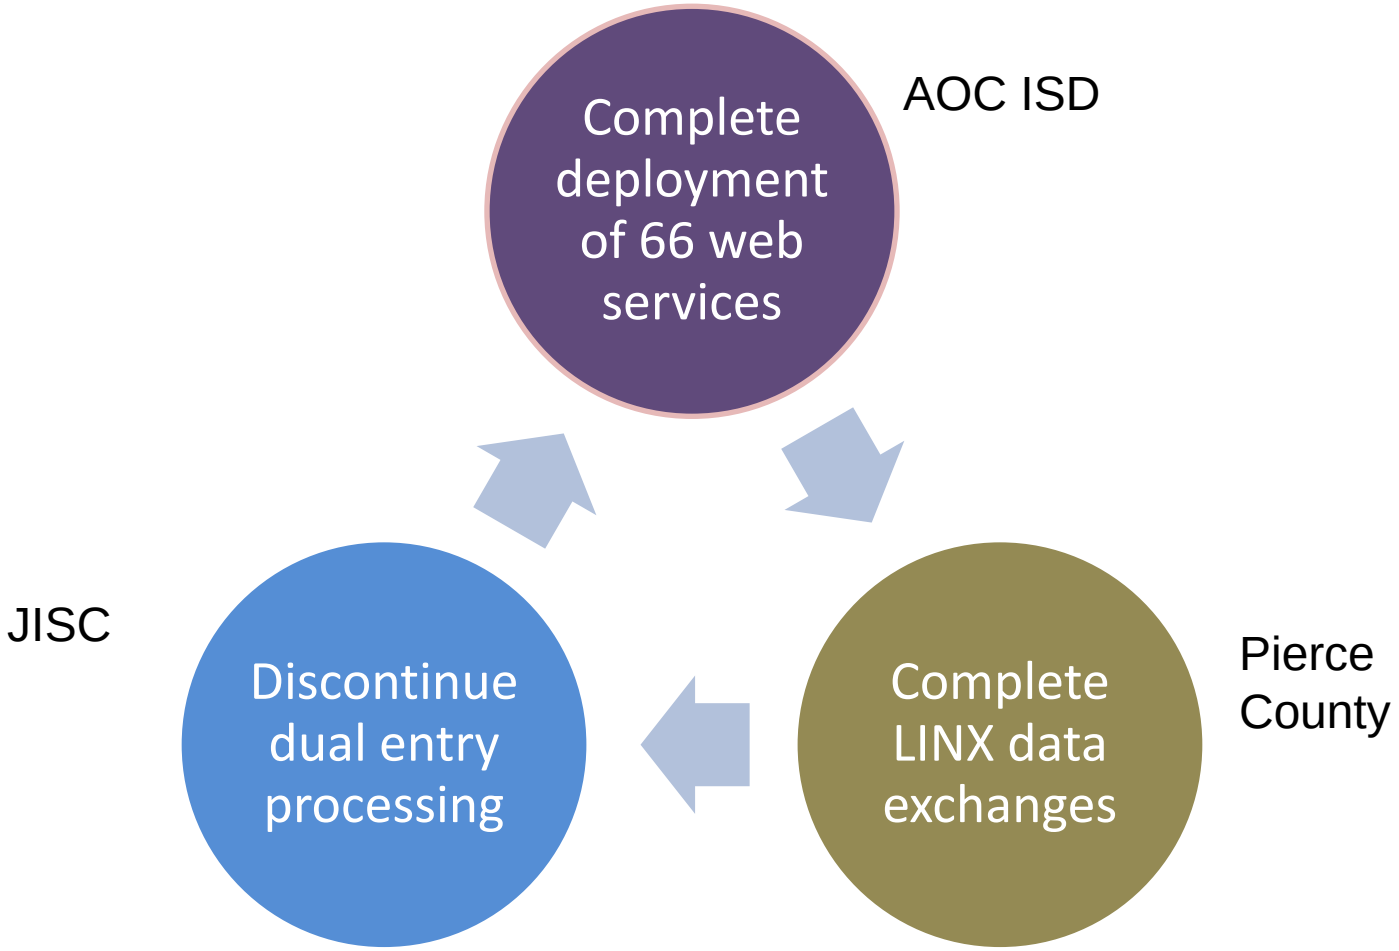

Active Project Issues

Low Urgency	Medium Urgency	High Urgency	Closed
0	0	3	0

High Urgency Issues Status

Issue	Urgency/Impact	Action
Turn around impacting schedule	High/Med	• Continue to monitor and adjust
Pierce Docket entry sequence causes erroneous case status in SCOMIS	High/High	• Changes to both the Pierce County sending services and the AOC receiving services
Field truncation	High/High	•Pierce County will apply truncation rules when generating the web service request

Next Steps

Milestone	Date
AOC deploys modified Docket Services	May 2013
Pierce County starts using Docket services	June 2013
AOC completes deployment of all 66 services	July 2013
AOC supports Pierce County and any other customers as they start consuming services	On-going
