Superior Court Case Management System (SC-CMS)

Project Update

Maribeth Sapinoso, Project Manager
Keith Curry, Deputy Project Manager

April 26, 2013

SC-CMS Project Status

- **Milestones Accomplished**
  - ✓ March 19, 2013 - Project Steering Committee voted unanimously to recommend AOC proceed into Contract Negotiations with Tyler Technologies, Inc.
  - ✓ March 22, 2013 - JISC voted unanimously to approve Project Steering Committee's recommendation.

SC-CMS Project Status

(Continued)

Contract Negotiations

- ✓ Subject Matter Experts Selected by Project Steering Committee
- Legal Team Meets with Tyler April 23-25, 2013
- Subject Matter Experts Meet with Tyler May 9-10, 2013
- Weekly Briefings will be provided to the Project Steering Committee

SC-CMS Project Status

(Continued)

Next Steps

- May/June 2013 – Finalize Contract Negotiations
- June 2013 – Project Steering Committee Recommends to the JISC Whether to Approve the Final Terms of the Contract
- June 2013 – JISC Decision Whether to Approve Project Steering Committee's Recommendation

Phase 1 - Acquisition

MILESTONE	DATE
✓ JISC Approval to Release RFP / RFP Published	June 2012
✓ Vendor Proposals Due	August 2012
✓ Evaluate & Score Written Responses	September 2012
✓ Steering Committee Confirms Top Ranked Vendors for Demos	September 2012
✓ Complete Vendor Demos	October 2012
✓ Steering Committee Confirms Top Ranked Vendors for Onsite Visits	October 2012
✓ Complete Onsite Visits	December 2012
✓ Notify Apparent Successful Vendor	January 2013
✓ Steering Committee Makes Recommendation to JISC	March 2013
Complete Contract Negotiations	May/June 2013
JISC Approval to Execute Contract	June 2013
Phase 1 Complete	June 2013

Phase 2 and Phase 3 - Next Steps

MILESTONES	DATE
✓ Court User Work Group Kick Off Meeting	January 2013
➢ Develop and Validate Court Business Process Models	In Progress
➢ Prepare AOC Technical Environment	In Progress
➢ Court Readiness Planning Activities	In Progress
Begin Identifying Interfaces Between SC-CMS and Local Court Applications	2nd Quarter 2013
Begin Selection of Pilot Court	2nd Quarter 2013
Begin Phase 2	June 2013
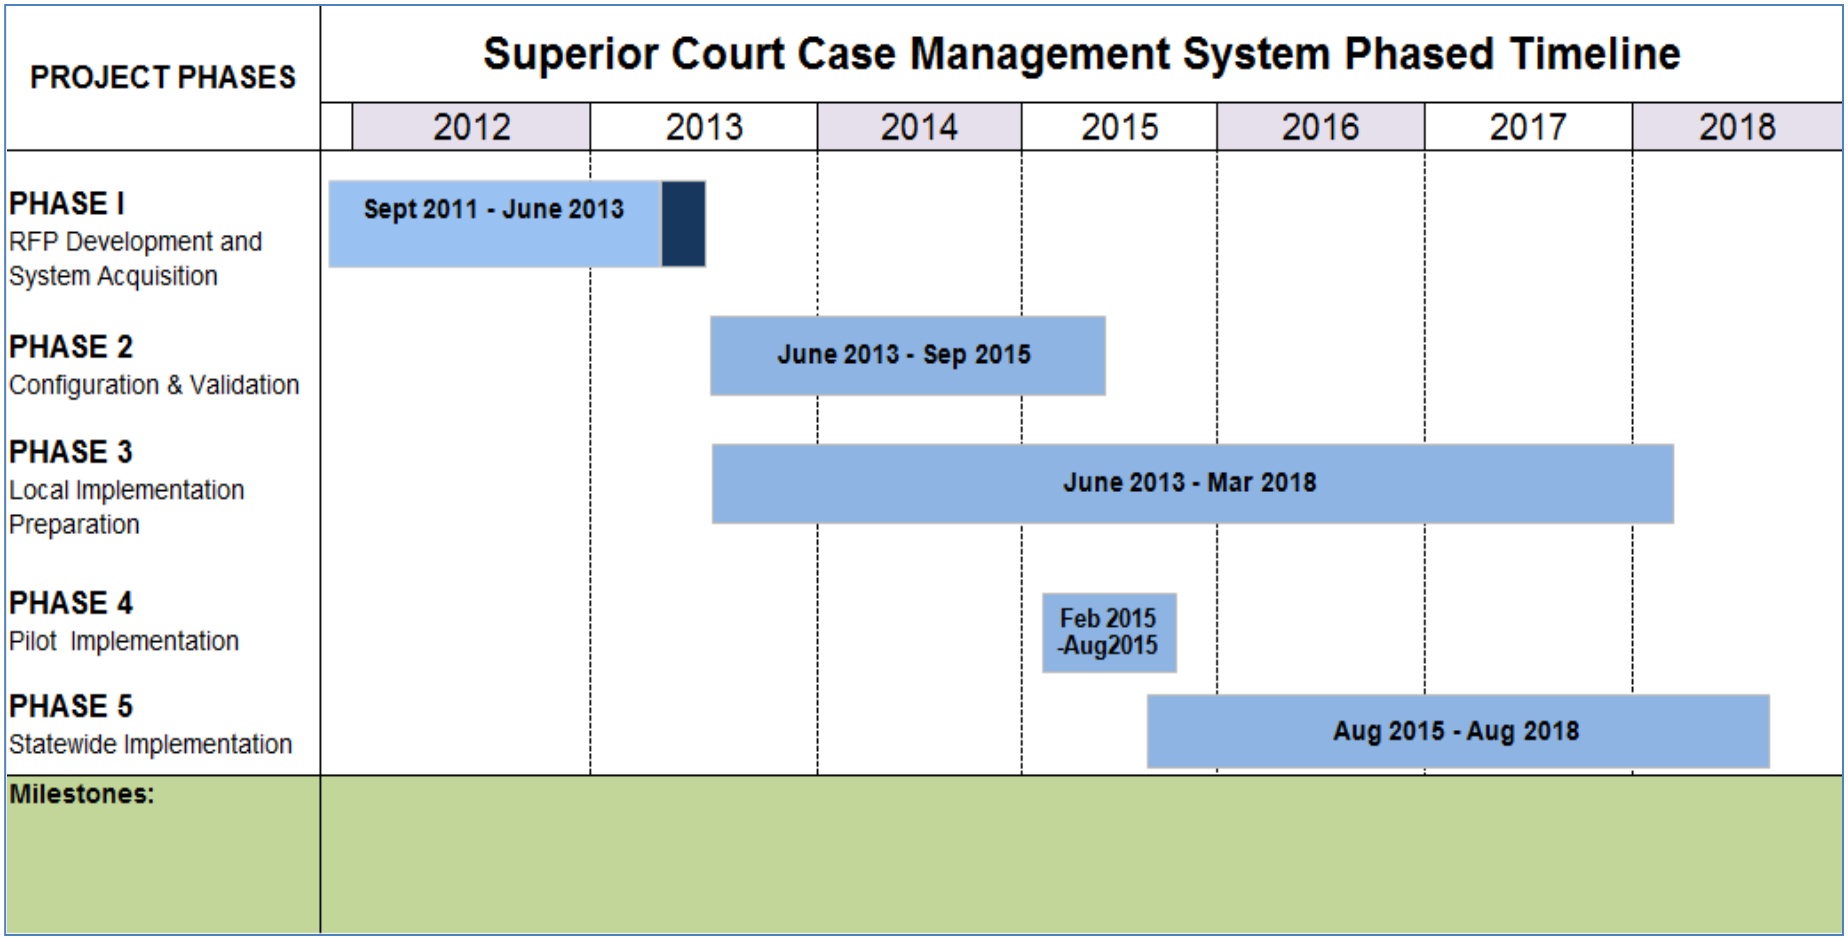
SC-CMS Project High Level Schedule
