Information Networking Hub (INH)

Project Update

Dan Belles, PMP - Project Manager
July 19, 2013

Recent Activities

Project Team Changes

- ✓ Joel Byford – Left for new position
- ✓ New Project Leads – Middleware/EDR

INH Middleware Data Exchanges (SC-CMS Ready)

- ✓ Implemented BizTalk Data Exchange Platform Enhancements
- ✓ Designed 4 new Data Exchanges
- ✓ Developed 21 new Data Exchanges
- ✓ Tested 11 Data Exchanges and resolved 6 defects

Enterprise Data Repository (EDR)

- Continued Database Models Review
- Continued Database Analysis and Solution Design

Schedule

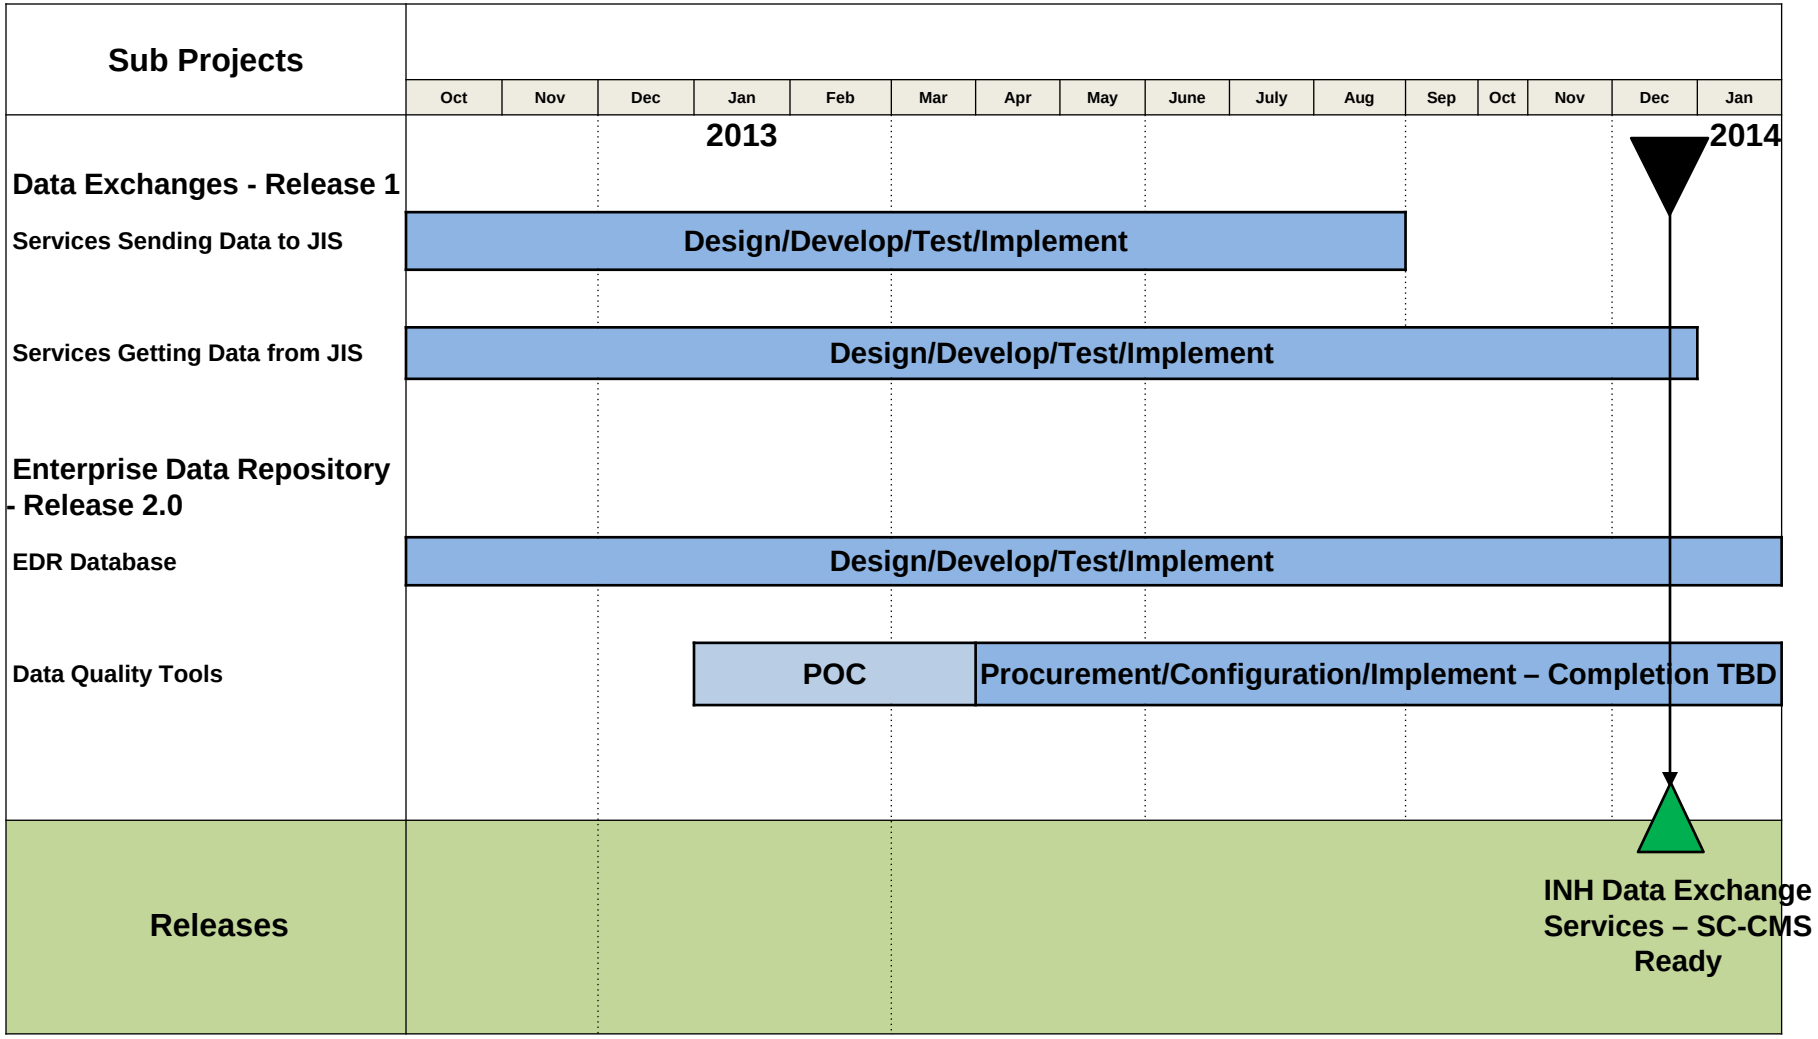
Sub Projects
Oct
Nov
Dec
Jan
Feb
Mar
Apr
May
June
July
Aug
Sep
Oct
Nov
Dec
Jan
2013
2014
Data Exchanges - Release 1
Services Sending Data to JIS
Design/Develop/Test/Implement
Services Getting Data from JIS
Design/Develop/Test/Implement
Enterprise Data Repository - Release 2.0
EDR Database
Design/Develop/Test/Implement
Data Quality Tools
POC
Procurement/Configuration/Implement – Completion TBD
Releases
INH Data Exchange Services – SC-CMS Ready

Active Project Risks

Total Project Risks		
Low Exposure	Medium Exposure	High Exposure
0	0	2

Significant Risks Status

Risk	Probability/Impact	Mitigation
Critical Project Inter-dependencies	High/High	•Inter-dependent Project Coordination Team (IPCT)
Services and EDR Integration with SC-CMS Application	High/High	•Collaborate with SC-CMS technical team and vendor to develop an interface integration plan

Active Project Issues

Total Project Issues			
Active	Monitor	Deferred	Closed
0	0	0	3

Significant Issues Status

Issue		Urgency/Impact	Action

Next Steps

Middleware Sub Project	
Milestone	Date
Develop Data Exchanges and BizTalk Enhancements	December 2013
Testing INH Services	December 2013
Resolve Defects/SC-CMS Ready	December 2013

Enterprise Data Repository Sub Project	
Milestone	Date
Complete Database Design Reviews	July 2013
Develop Security Model	September 2013
Design Database Solution	September 2013
Develop Physical Database	January 2014
Implement Data Quality Automation	To Be Determined
