Superior Court Data Exchange

Project Update

Mike Walsh - Project Manager

July 19, 2013

Pierce County Update

- Pierce County has notified AOC that the county's Technology Investment Board has directed the county IT department to complete work on 6 of 66 SCDX data exchanges.
  - All work on the remaining 60 data exchanges will be put on hold – indefinitely.
  - They estimated that it would require Pierce to devote 3,000 hours to complete all 66 SCDX data exchanges.

Recent Activities

Pierce County data exchange on boarding:

✓ Docket Modifications to handle LINX docket sequencing deployed

- Problem discovered in Civil Case validation: Case initiation with well-identified persons results in duplicate docket entries being added to cases
  - ❑ AOC is making a small modification to SCOMIS to address this issue
  - ❑ Pierce County SCDX start up is delayed until modification is implemented

Recent Activities

All SCDX web services have now completed initial testing by AOC

Increment 3 Status (12 web services)

- ✓ All 12 web services approved and deployed

Increment 4 Status (25 web services)

- ✓ All 25 web services approved and deployed

Schedule

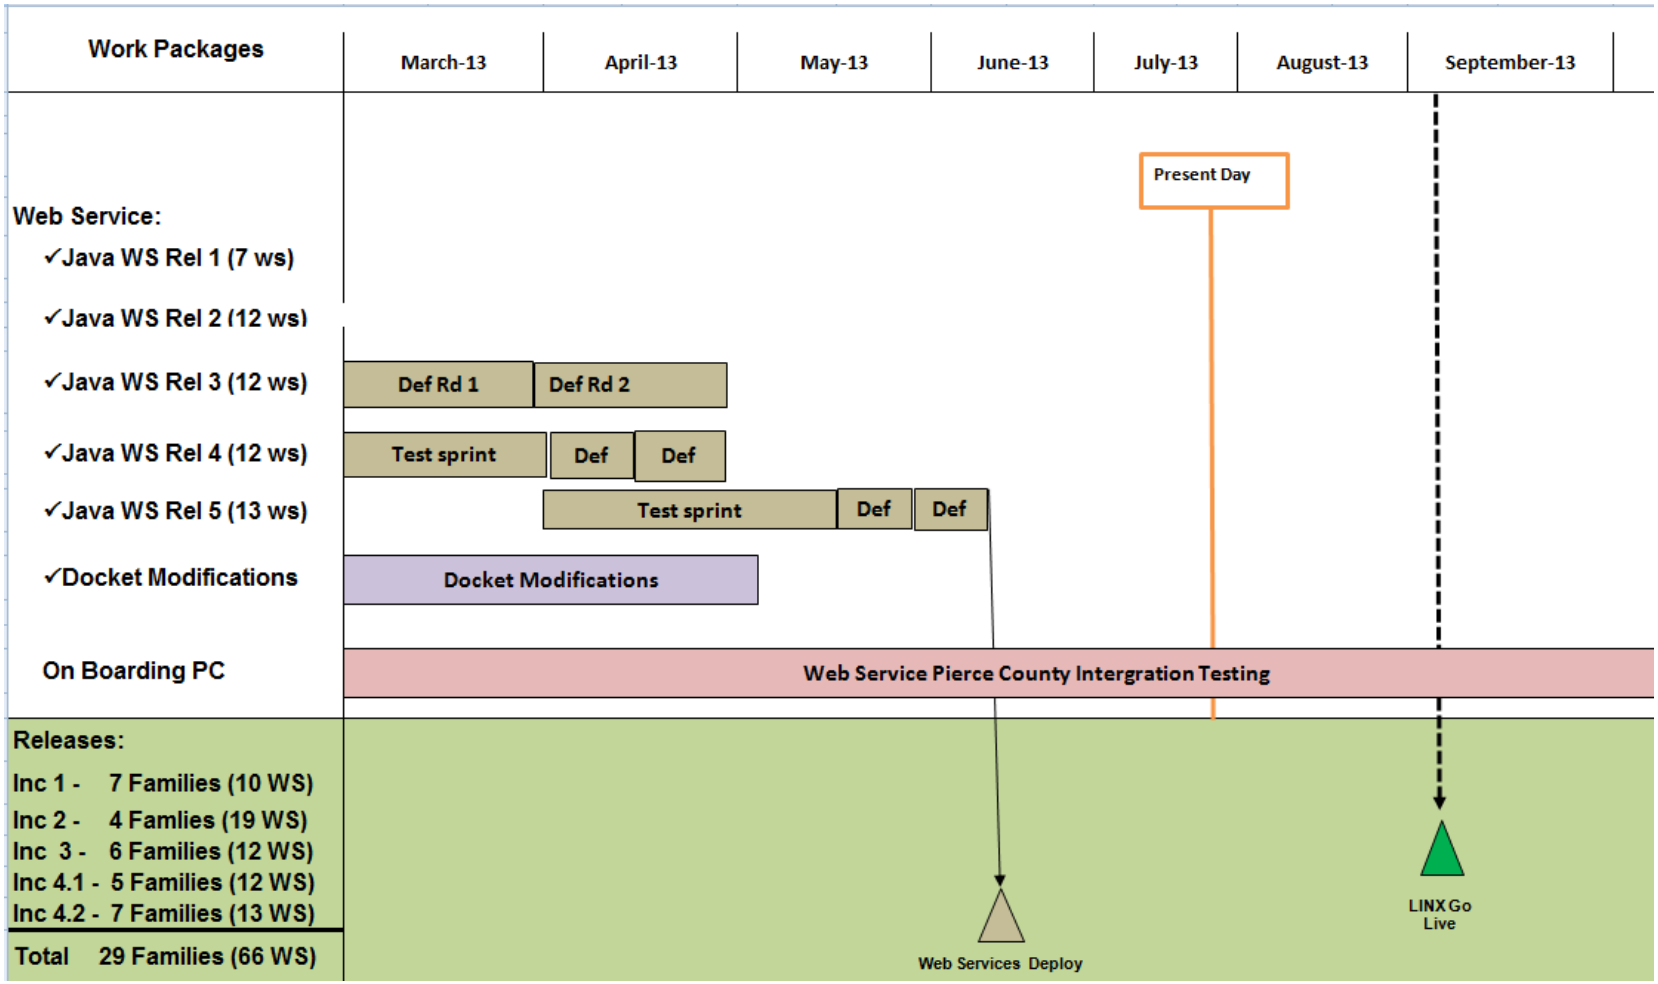
Work Packages
March-13
April-13
May-13
June-13
July-13
August-13
September-13
Present Day
Web Service:
✓Java WS Rel 1 (7 ws)
✓Java WS Rel 2 (12 ws)
✓Java WS Rel 3 (12 ws)
Def Rd 1
Def Rd 2
✓Java WS Rel 4 (12 ws)
Test sprint
Def
Def
✓Java WS Rel 5 (13 ws)
Test sprint
Def
Def
✓Docket Modifications
Docket Modifications
On Boarding PC
Web Service Pierce County Intergration Testing
Releases:
Inc 1 - 7 Families (10 WS)
Inc 2 - 4 Famlies (19 WS)
Inc 3 - 6 Families (12 WS)
Inc 4.1 - 5 Families (12 WS)
Inc 4.2 - 7 Families (13 WS)
Total 29 Families (66 WS)
Web Services Deploy
LINX Go Live

When are we done?

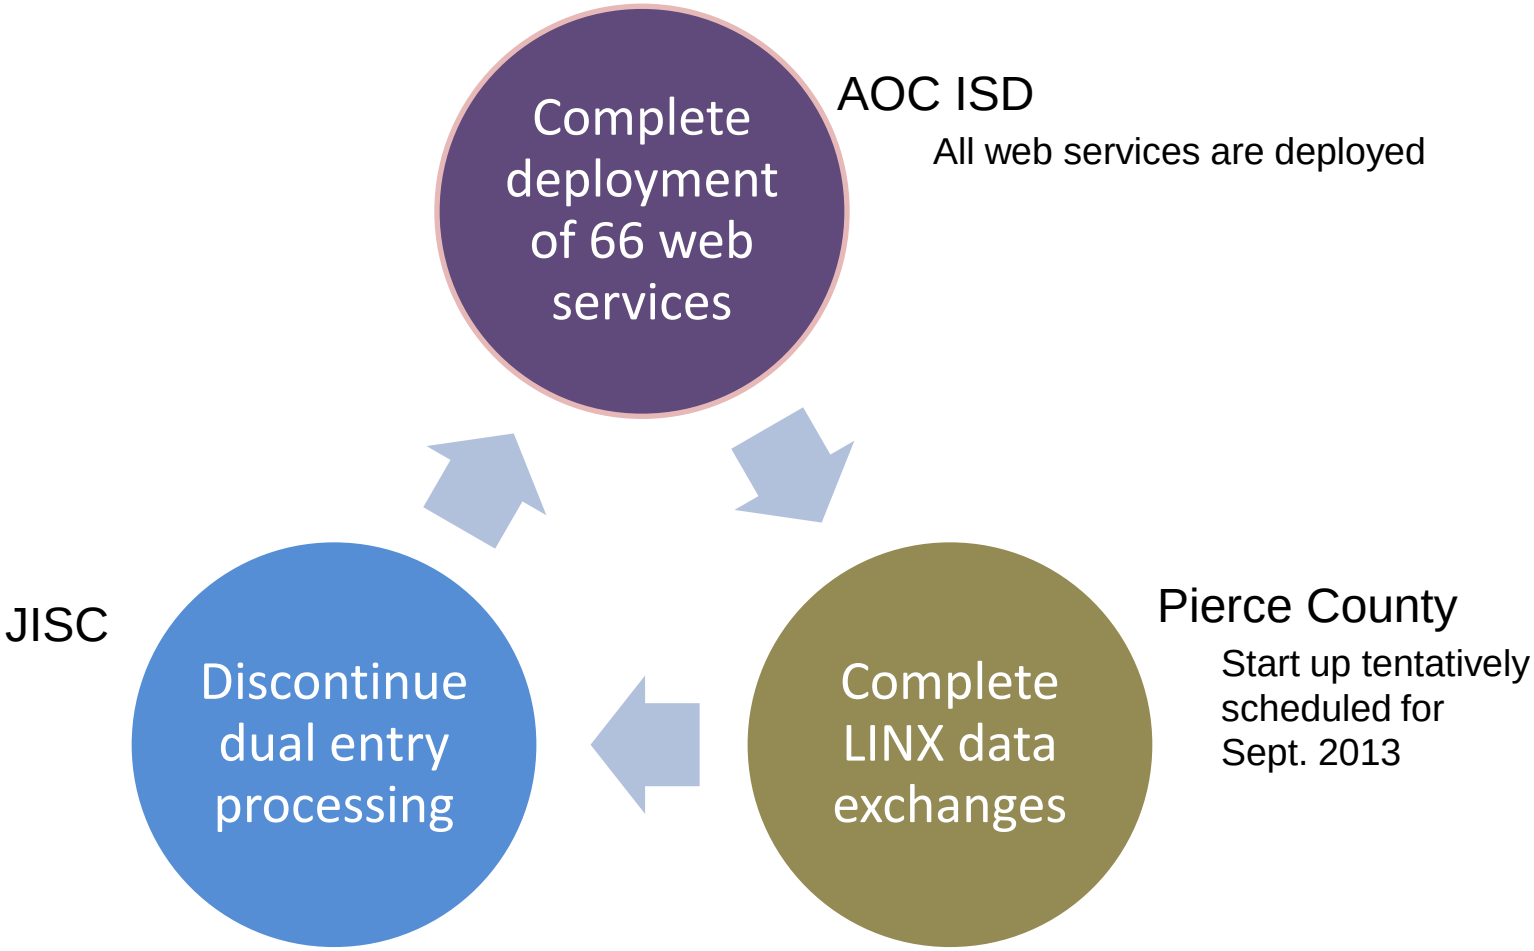

Active Project Issues

Low Urgency	Medium Urgency	High Urgency	Closed
0	0	3	0

High Urgency Issues Status

Issue	Urgency/Impact	Action
Pierce Docket entry sequence causes erroneous case status in SCOMIS	High/High	• Changes to both the Pierce County sending services and the AOC receiving services
SCDX team lacks SME for business guidance	High/High	• Accept risk and continue to use available ISD resources where appropriate
Docket service integration problem with judgment dockets	High/High	• Review mitigation options with ISD leadership

Next Steps

Milestone	Date
Pierce County starts using Docket services	September 2013
AOC supports Pierce County, King County and any other customers as they start consuming services	On-going
