Superior Court Data Exchange

Project Update

Mike Walsh - Project Manager

September 6, 2013

Recent Activities

Pierce County data exchange on-boarding:

- ✓ AOC has deployed a small change to SCOMIS to eliminate issue Pierce County encountered with duplicate docket entries
- ✓ AOC also deployed new security protocol to comply with new Pierce County standard
- ✓ Pierce County resumes testing
- ❑ Pierce County's implementation of all 6 services is planned for September 2013

Schedule

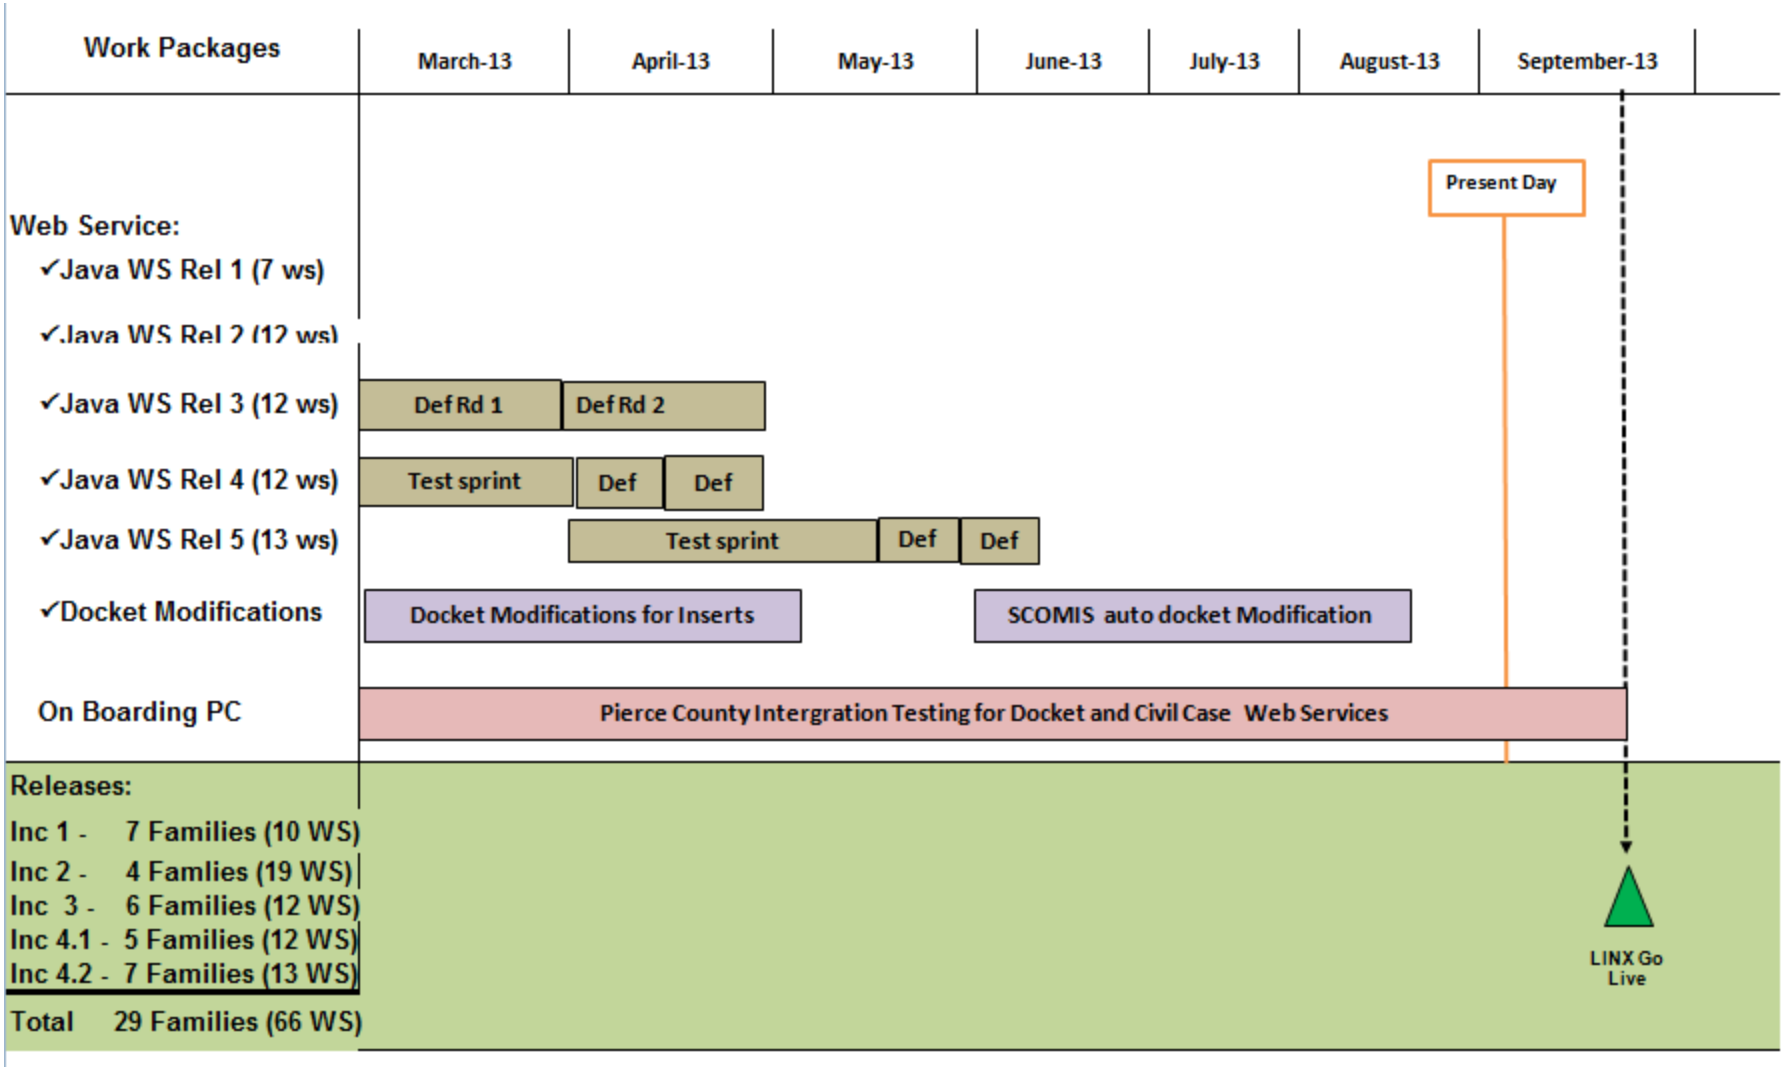
Work Packages
March-13
April-13
May-13
June-13
July-13
August-13
September-13
Present Day
Web Service:
✓Java WS Rel 1 (7 ws)
✓Java WS Rel 2 (12 ws)
✓Java WS Rel 3 (12 ws)
Def Rd 1
Def Rd 2
✓Java WS Rel 4 (12 ws)
Test sprint
Def
Def
✓Java WS Rel 5 (13 ws)
Test sprint
Def
Def
✓Docket Modifications
Docket Modifications for Inserts
SCOMIS auto docket Modification
On Boarding PC
Pierce County Intergration Testing for Docket and Civil Case Web Services
Releases:
Inc 1 - 7 Families (10 WS)
Inc 2 - 4 Famlies (19 WS)
Inc 3 - 6 Families (12 WS)
Inc 4.1 - 5 Families (12 WS)
Inc 4.2 - 7 Families (13 WS)
Total 29 Families (66 WS)
LINX Go Live

Active Project Issues

Low Urgency	Medium Urgency	High Urgency	Closed
0	0	2	1

High Urgency Issues Status

Issue	Urgency/Impact	Action
SCDX team does not have LINX business knowledge – this may be an ongoing issue for on-boarding activities of other services	High/High	• Accept risk and continue to use available ISD and Pierce County court resources where appropriate
Docket service integration problem with judgment dockets	High/High	• AOC has implemented SCOMIS change to correct issue •Awaiting verification by Pierce

Next Steps

Milestone	Date
Pierce County starts using Docket and Civil Case services	September 2013
AOC supports Pierce County, King County and any other customers as they start consuming services	On-going
Post implementation follow up	December 2013
