Superior Court Case Management System (SC-CMS)

Project Update

Maribeth Sapinoso, AOC Project Manager
Marie Constantineau, AOC Deputy Project Manager

October 24, 2014

Recent Activities

- ✓ DMS Responses as of October 8, 2014:
  - 30 Counties have responded
    - 12 Odyssey DMS
    - 10 Link Only (“Pointer”)
    - 5 Lack of agreement
    - 3 Undecided
    - 7 Awaiting response

DMS Selection as of October 8, 2014

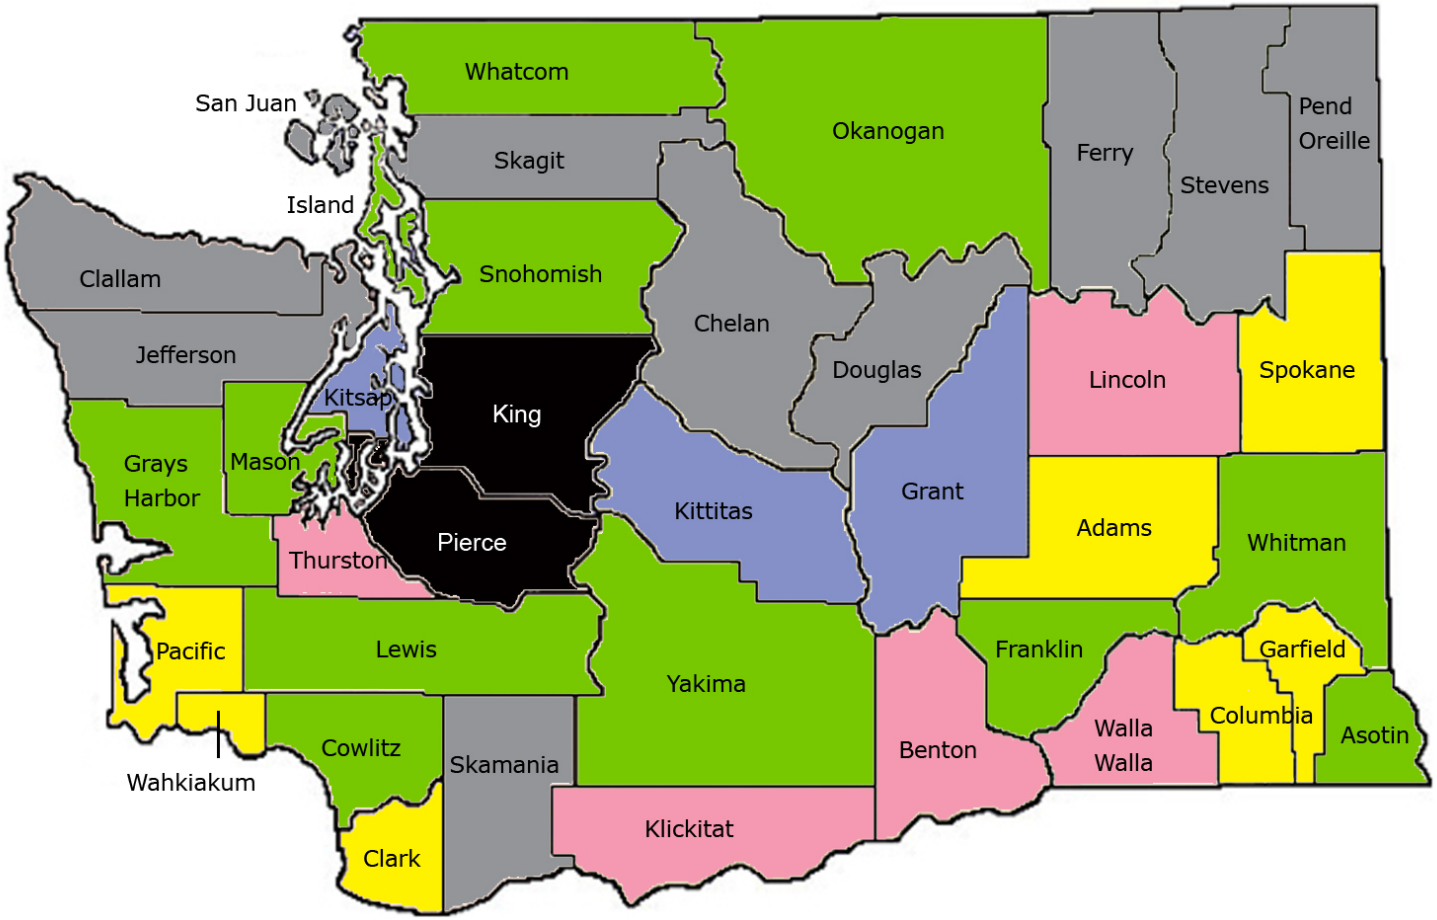

= Odyssey DMS = Link Only (Pointer) = Lack of Agreement = Undecided

= Awaiting Response

Recent Activities *(cont'd)*

- ✓ Project Steering Committee Decisions
  - ✓ Thurston County was selected as an Early Adopter.
  - ✓ Snohomish County's request to be a Pilot was not approved.
  - ✓ Benton, Klickitat, and Walla Walla, at their request, were withdrawn as Early Adopters.

Pilot: Lewis County

Early Adopters: Franklin, Thurston, Yakima

- ✓ Identified order of statewide rollout plan

Recent Activities *(cont'd)*

- ✓ Conducted Kick Off meeting with Early Adopters – September 16, 2014.
- ✓ Completed first Pilot stakeholder meeting – September 22, 2014.
- ✓ Completed second data conversion push
  - o Total *Party* Records Converted: **10.4 Million**
  - o Total *Case* Records Converted: **888,241**
- ✓ Completed first data conversion training/review with Pilot power users – October 7-9, 2014.

Work In Progress

- Customizing “Help” in Odyssey for the State of Washington.
- Preparing project update for upcoming Association of City and County Information Systems (ACCIS) conference – October 22, 2014.
- Preparing for on site kickoff with Early Adopter technical staff – November 5 & 6, 2014.
- Scheduling meetings with 3rd party DMS vendors for Link Only (“Pointer”).

Next Steps

- Accept delivery of Tyler integration and application development
- Begin unit testing of application development
- Develop DMS prototype for Link Only option
- Complete Pilot site business process reviews
- Prepare for integration testing

Phase 3 – Pilot Implementation

MILESTONES or PROJECT DELIVERABLES	CURRENT PLAN DATE
✓ Second Data Conversion Push	August 2014
✓ DMS Intent decisions received	October 2014
✓ Third Data Conversion Push	October 2014
Tyler Development (Integration) Work Completed	October 2014
Integration Testing Begins	Jan – Mar 2015
Fourth Data Conversion Push	January 2015
Local Court Configuration Completed	January 2015
Integration Testing Completed	May 2015
Pilot Mock Go-Live	February 2015
Pilot End User Training Complete	May 2015
Pilot Go-Live Conversion Activities Begin	June 2015
