Courts of Limited Jurisdiction Case Management System (CLJ-CMS)

Project Update

Garret Tanner
CLJ-CMS Project Manager

December 2, 2022

Project Scope

Three components:

- eFile & Serve (Odyssey File & Serve)
- Enterprise Justice (Odyssey)
- Enterprise Supervision (Tyler Supervision)

Go Live Delay

- **Pilot Courts Go Live event delayed from October 17, 2022**

- **Next Steps:**
  - ❖ Complete Solution Validation (end-to-end test) to ensure the system meets the needs of CLJs
  - ❖ Complete Data Exchanges with Justice Partners
    - Enterprise Data Repository
    - DOL / Person Lookup
    - eCitation & VRV
    - Etc.
  - ❖ Review Go Live tasks and assumptions to identify a new date for Pilot Court Go Live

Project Timeline

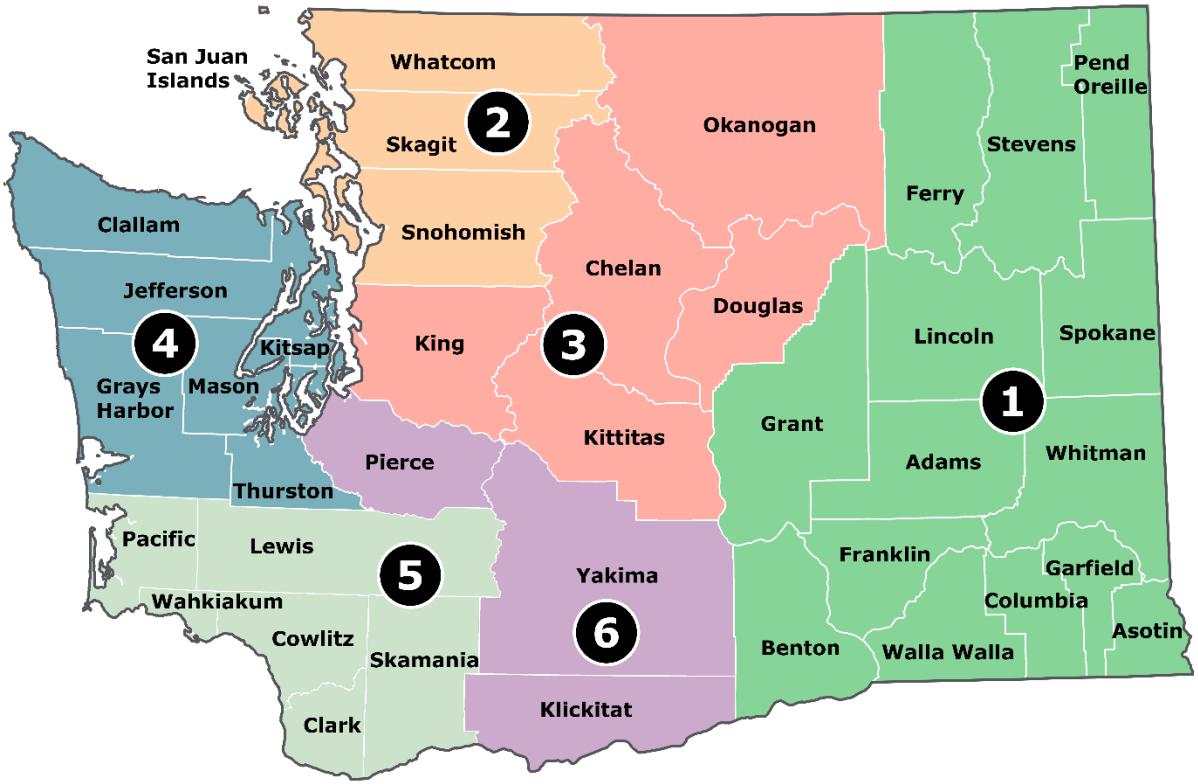

Counties by Phase

Pilot Courts
Pierce District, Tacoma Municipal,
Gig Harbor Municipal, Fircrest/Ruston Municipal

Phase 1
Eastern Washington - Adams, Asotin, Benton, Columbia, Ferry, Franklin, Garfield, Grant, Lincoln, Pend Oreille, Spokane, Stevens, Walla Walla, and Whitman

Phase 2
North Washington - Island, San Juan, Skagit, Snohomish, and Whatcom

Phase 3
North Central Washington - Chelan, Douglas, King Municipals, Kittitas, and Okanogan

Phase 4
Western Washington - Clallam, Grays Harbor, Jefferson, Kitsap, Mason, and Thurston

Phase 5
Southwest Washington - Clark, Cowlitz, Lewis, Pacific, Skamania, and Wahkiakum

Phase 6
South Central Washington - Klickitat, remainder of Pierce Municipals, and Yakima

Project Timeline

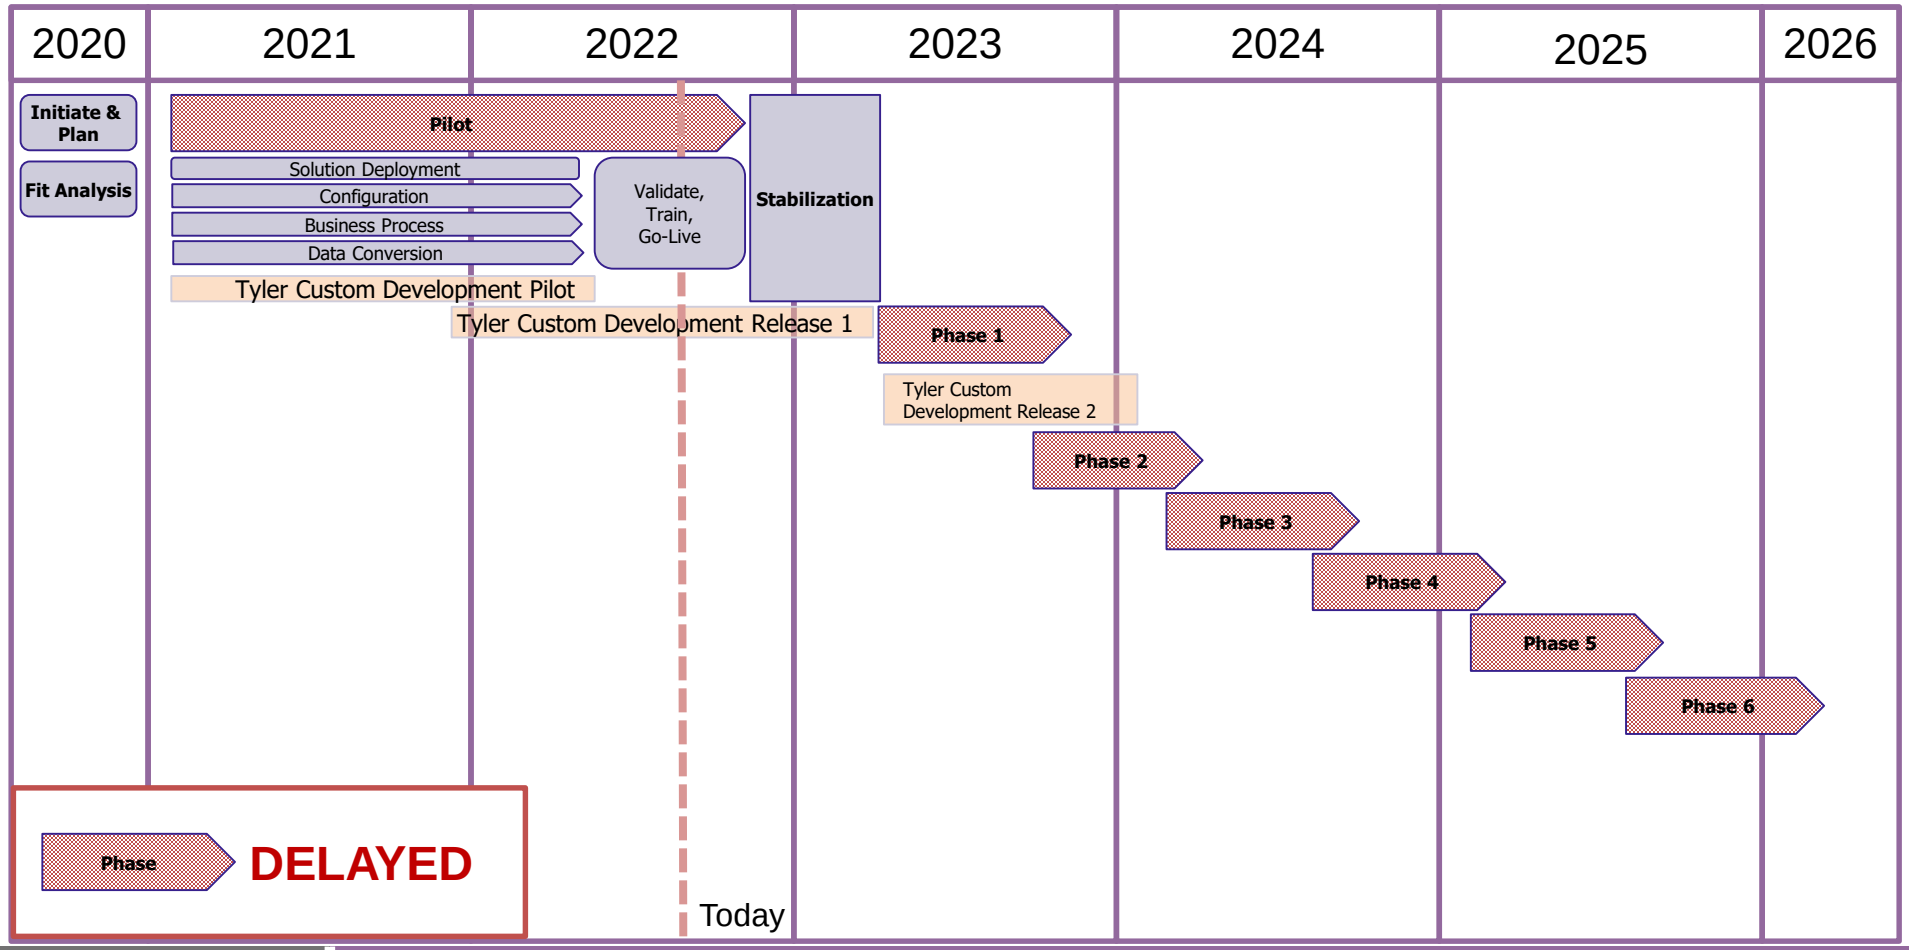

Solution Validation Status

Focus Area	Status
eFile & Serve	Ready
Development Enterprise Justice	Awaiting Fixes
Development Enterprise Supervision	**Awaiting Fixes**
Configuration Enterprise Justice	**Awaiting Fixes**
Configuration Supervision	Awaiting Fixes
Data Conversion Enterprise Justice	Ready
Data Conversion Enterprise Supervision	Awaiting Fixes
Data Exchanges (EDR)	In Development
Data Exchanges (Other)	In Development
Enterprise Justice Financials	Ready
Enterprise Justice Reporting	In Development
Enterprise Supervision Reporting	Testing
Pilot Court Readiness	Ready

Risk to Timeline
Low Risk
Medium Risk
High Risk

Recent eFiling Activity

- ✓ eFile testing for all Pilot Courts
- ❖ eFile marketing website and updates underway

Recent CMS Activity

- ❖ Pilot Courts building forms for local use
- ✓ Data Push 6 Completed
- ✓ Data Review 6 Completed
- ❖ Preparations for Data Push 7
  - Expected at start of Solution Validation

Project Outreach

- Continue project outreach and promotion
- Continue working with Pilot Courts on internal communications

Work in Progress

- Continue working Solution Validation "punch list"
- Continue testing Pilot Development from Tyler Technologies
  - ✓ eFile
  - Enterprise Justice
  - Enterprise Supervision

Tyler Releases

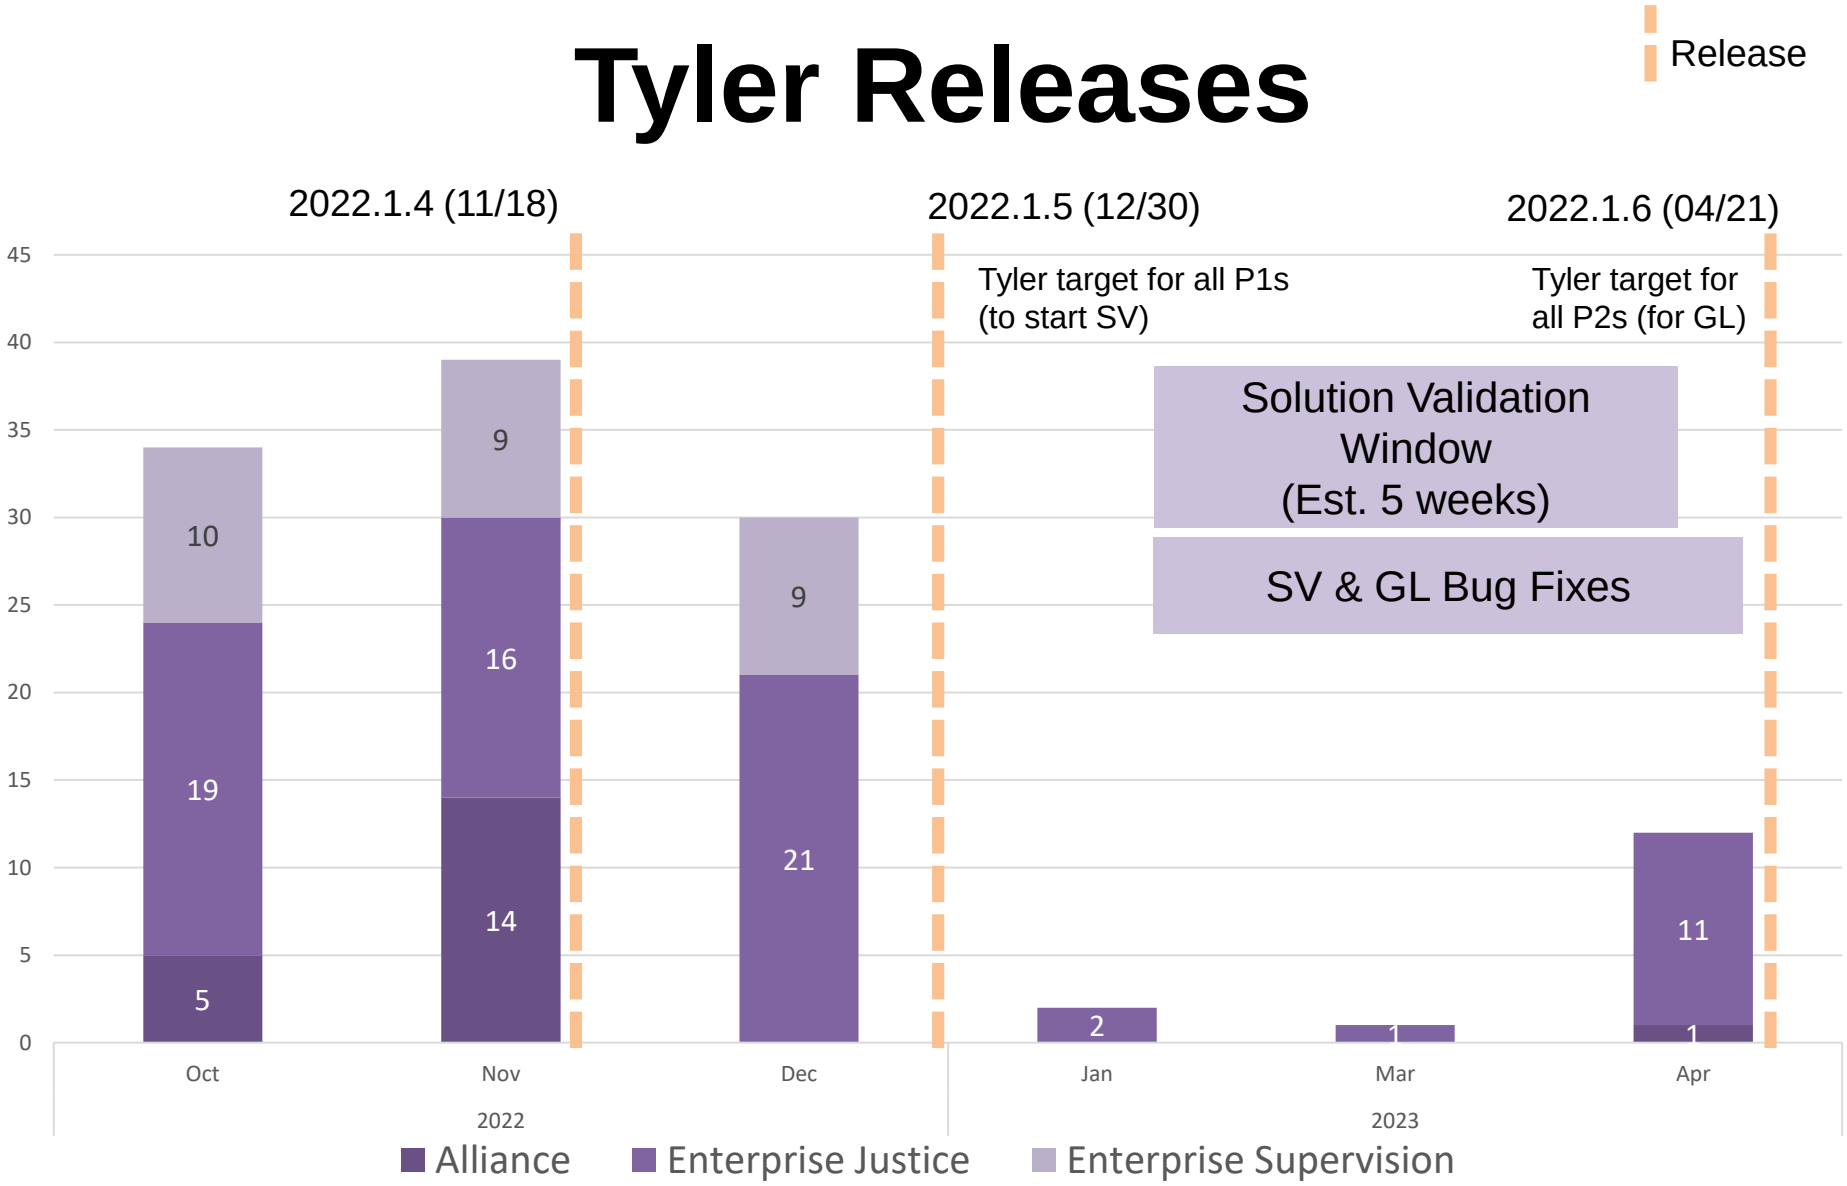

Project Issues – December 2022

Active Issues	
Issue	Mitigation
Pilot Go Live – Delaying Pilot Go Live will impact future Phases.	(August 26, 2022) Tyler / AOC working and estimating remaining "go live" for post-Solution Validation.
Solution Validation (Pilot) – Delaying Solution Validation will delay Pilot Go Live and beyond.	**(November 1, 2022) Tyler targets December 30, 2022 for resolution of all Priority 1 issues (for Solution Validation start).**
Local Rule – In order for eFiling to be mandatory courts need to enact a local rule. Some courts could choose not to enact the rule or make eFiling mandatory.	(April 5, 2022) DMCJA is championing a Statewide rule for mandatory eFiling. Pilot Courts will need to enact a local rule in the meantime.
Enterprise Justice version to be used (Pilot) – In November 2021, Tyler determined that Enterprise Justice 2019 would not be compatible with some of the mandatory requirements.	(February 1, 2022) In January the vendor formally recommend Enterprise Justice version 2022.1 be used for Pilot Court Go-Live. Version 2022.1 has been installed on our Development environment and is currently being reviewed by our Quality Assurance and Business Analyst teams.

Project Issues – December 2022

Active Issues	
Issue	Mitigation
Enterprise Supervision/Enterprise Justice Integrations (Alliance) – The two products are not yet seamlessly integrated.	**(November 15, 2022) Tyler Technologies estimates resolution of all Priority 1 Alliance issues by December 30, 2022.**
Staffing / Hiring – CLJ-CMS has been unable to fill several key positions. As of December 2022, CLJ-CMS has 9 project positions open. If these positions are not filled there may be impacts to the schedule.	**(November 11, 2022) 7 pre-Pilot vacancies. Additional AOC resources have been re-assigned to CLJ-CMS.**

Project Risks – December 2022

Total Project Risks			
Low Probability	Moderate Probability	High Probability	Closed
0	3	3	19

High Risks Status		
Risk	Probability/Impact	Mitigation
Equipment Funding – Additional funds may be needed to assist some courts with the local equipment purchases.	Moderate/Moderate	(September 22, 2020) If the CLJ-CMS project uses a similar funding model to the SC-CMS, then there are additional complexities to consider. There are significantly more CLJ courts which adds to the need.
Enterprise Supervision – Tyler has not done a statewide implementation of their new Supervision module. Previous implementations have always been with individual probation departments.	High/Major	(February 17, 2021) AOC PM and Tyler PM are working closely to best align the process for a statewide implementation vs. an individual one.

Project Risks – December 2022

High Risks Status		
Risk	Probability/Impact	Mitigation
Third Party Integrations – Some courts have local systems that they would like integrated with Enterprise Justice.	High/High	(August 26, 2022) JISC has approved ITG 1340 to build an enterprise integration platform pending funding. ITG 1345 has been approved by CIO pending ITG 1340 funding.
Enterprise Justice version to be used (Phase 1) – In November 2021, Tyler determined that Enterprise Justice 2019 would not be compatible with some of the mandatory requirements.	High/High	**(November 9, 2022) Tyler now recommends version 2024.x for Phase 1. Upgrade needs to be analyzed and planned for.**

Project Risks – December 2022

High Risks Status		
Risk	Probability/Impact	Mitigation
Efficiency Concerns – It is expected that some users will be experience short-term reduced efficiencies when compared against legacy systems.	Moderate/Moderate	(May 17, 2022) It is well documented that it is common to experience a short-term efficiency slump when introducing new systems or business processes. Concerns that working in the new system will be slower than legacy systems are still present and will be addressed through training and change management activities.
Performance Issues – It is possible that users will feel that Enterprise Justice works less efficiently than the legacy system due to changing processes and procedures.	Moderate/Moderate	(August 1, 2022) Performance of version 2022.1.x is improved over 2019.x. Concerns that the system will be slower than Legacy systems are still present and will be addressed with training and change management activities. CLJ-CMS benchmark testing scheduled.

Next Steps

Milestone	Date
Begin Solution Validation	TBD
Go-live Pilot courts	TBD

Independent Quality Assurance Update

Mr. Allen Mills
Bluecrane, Inc.
